


EDC/TACOA PROJECT LM 6000 SIMPLE CYCLE PROJECT PROJECT EXECUTIVE SCHEDULE																																										
ID		Task Name	Duration	Start	Finish	% Complete	9, '09							Aug 16, '09							Aug 23, '09							Aug 30, '09							Sep 6, '09							Sep 1
							M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	
1		EDC / TACOA Project - 2 Unit LM6000 Site	252 days	Mon 8/10/09	Tue 6/1/10	3%																																				
2		Initial Date	1 day	Mon 10/5/09	Mon 10/5/09	0%																																				
3		Milestone Dates (Key Dates)	50 days	Mon 8/24/09	Mon 10/12/09	29%																																				
4		Initial Date	1 day	Mon 10/5/09	Mon 10/5/09	0%																																				
5		Backfeed Power Available	1 day	Mon 10/12/09	Mon 10/12/09	0%																																				
6		Natural Gas Available	1 day	Mon 10/12/09	Mon 10/12/09	0%																																				
7		Raw Water Available	1 day	Mon 10/12/09	Mon 10/12/09	0%																																				
8		Telephone & Internet Service Available	1 day	Mon 10/12/09	Mon 10/12/09	0%																																				
9	✓	Construction Power Connection Available	1 day	Fri 8/28/09	Fri 8/28/09	100%																																				
10	✓	Construction Permit	1 day	Mon 8/24/09	Mon 8/24/09	100%																																				
11		Payment milestones	172 days	Mon 10/5/09	Wed 4/28/10	0%																																				
12		Project Kickoff	1 day	Mon 10/5/09	Mon 10/5/09	0%																																				
13		Milestone 1 - Civil Works GTG foundation poured	1 day	Mon 10/26/09	Mon 10/26/09	0%																																				
14		MileStone 2 - Gas Turbine set on Foundation	1 day	Sun 11/15/09	Sun 11/15/09	0%																																				
15		Milestone 3 - Gas Turbine Erection complete	1 day	Sat 12/5/09	Sat 12/5/09	0%																																				
16		Milestone 4 - Mechanical Complete	1 day	Wed 1/27/10	Wed 1/27/10	0%																																				
17		Milestone 5 - Electrical Complete	1 day	Wed 1/27/10	Wed 1/27/10	0%																																				
18		Milestone 6 - Precommissioning complete	1 day	Wed 3/24/10	Wed 3/24/10	0%																																				
19		Milestone 7 - Plant commissioning and Testing complete	1 day	Wed 4/28/10	Wed 4/28/10	0%																																				
20		Engineering	53 days	Mon 8/10/09	Thu 10/1/09	14%																																				
21	✓	Conceptual & Major Equipment Specs	10 days	Tue 8/11/09	Thu 8/20/09	100%																																				
22	✓	Site Survey	2 days	Fri 8/21/09	Sat 8/22/09	100%																																				
23	✓	Soil Boring test	2 days	Mon 8/31/09	Tue 9/1/09	100%																																				
24		Civil and foundation engineering	21 days	Wed 9/2/09	Tue 9/22/09	0%																																				
25		Issue Foundation for Construction Drawings	2 days	Wed 9/23/09	Thu 9/24/09	0%																																				
26		Detailed Engineering	40 days	Fri 8/21/09	Tue 9/29/09	0%																																				
27		Bulk Material Specs and PO's	20 days	Mon 8/10/09	Sat 8/29/09	0%																																				
28		Issue for Construction Drawings	2 days	Wed 9/30/09	Thu 10/1/09	0%																																				
29		Procurement	60 days	Fri 8/21/09	Mon 10/19/09	0%																																				
30		Buildings	12 wks	Fri 8/21/09	Mon 10/19/09	0%																																				
31		BOP Mechanical	1.55 mons	Tue 9/1/09	Thu 10/1/09	0%																																				
32		BOP Electrical	1.55 mons	Tue 9/1/09	Thu 10/1/09	0%																																				
33		Transportation	30 days	Mon 10/12/09	Tue 11/10/09	0%																																				
34		GTG Package 100	30 days	Mon 10/12/09	Tue 11/10/09	0%																																				
35		GTG Package 200	30 days	Mon 10/12/09	Tue 11/10/09	0%																																				
36		Construction	148 days	Mon 8/24/09	Tue 1/26/10	2%																																				
37		Mobilize to Site	26 days	Mon 8/24/09	Fri 9/18/09	40%																																				
38		Civil Work	27 days	Sat 9/19/09	Thu 10/15/09	0%																																				
39		Site Preparation	20 days	Sat 9/19/09	Thu 10/8/09	0%																																				
40		Excavation & Grading	7 days	Fri 10/9/09	Thu 10/15/09	0%																																				
41		Install Perimeter Fence	12 days	Sat 9/19/09	Wed 9/30/09	0%																																				
42		Power Island Foundations	15 days	Fri 10/16/09	Fri 10/30/09	0%																																				
43		GTG 100	10 days	Fri 10/16/09	Sun 10/25/09	0%																																				
44		GTG 200	10 days	Fri 10/16/09	Sun 10/25/09	0%																																				
45		GSU 100	5 days	Mon 10/26/09	Fri 10/30/09	0%																																				
46		GSU 200	5 days	Mon 10/26/09	Fri 10/30/09	0%																																				
47		BOP Foundations	15 days	Fri 10/16/09	Fri 10/30/09	0%																																				
48		Unit Building	10 days	Fri 10/16/09	Sun 10/25/09	0%																																				
49		Substation	10 days	Fri 10/16/09	Sun 10/25/09	0%																																				
50		Substation Bldg																																								


EDC/TACO PROJECT
LM 6000 SIMPLE CYCLE PROJECT
PROJECT EXECUTIVE SCHEDULE

[illegible]


Project: EDC / TACOALM6000 Project Date: Tue 10/6/09	Critical		Task		Baseline		Milestone		Project Summary		Deadline	
	Critical Split		Split		Baseline Split		Summary Progress		External Tasks			
	Critical Progress		Task Progress		Baseline Milestone		Summary		External Milestone			

[illegible]

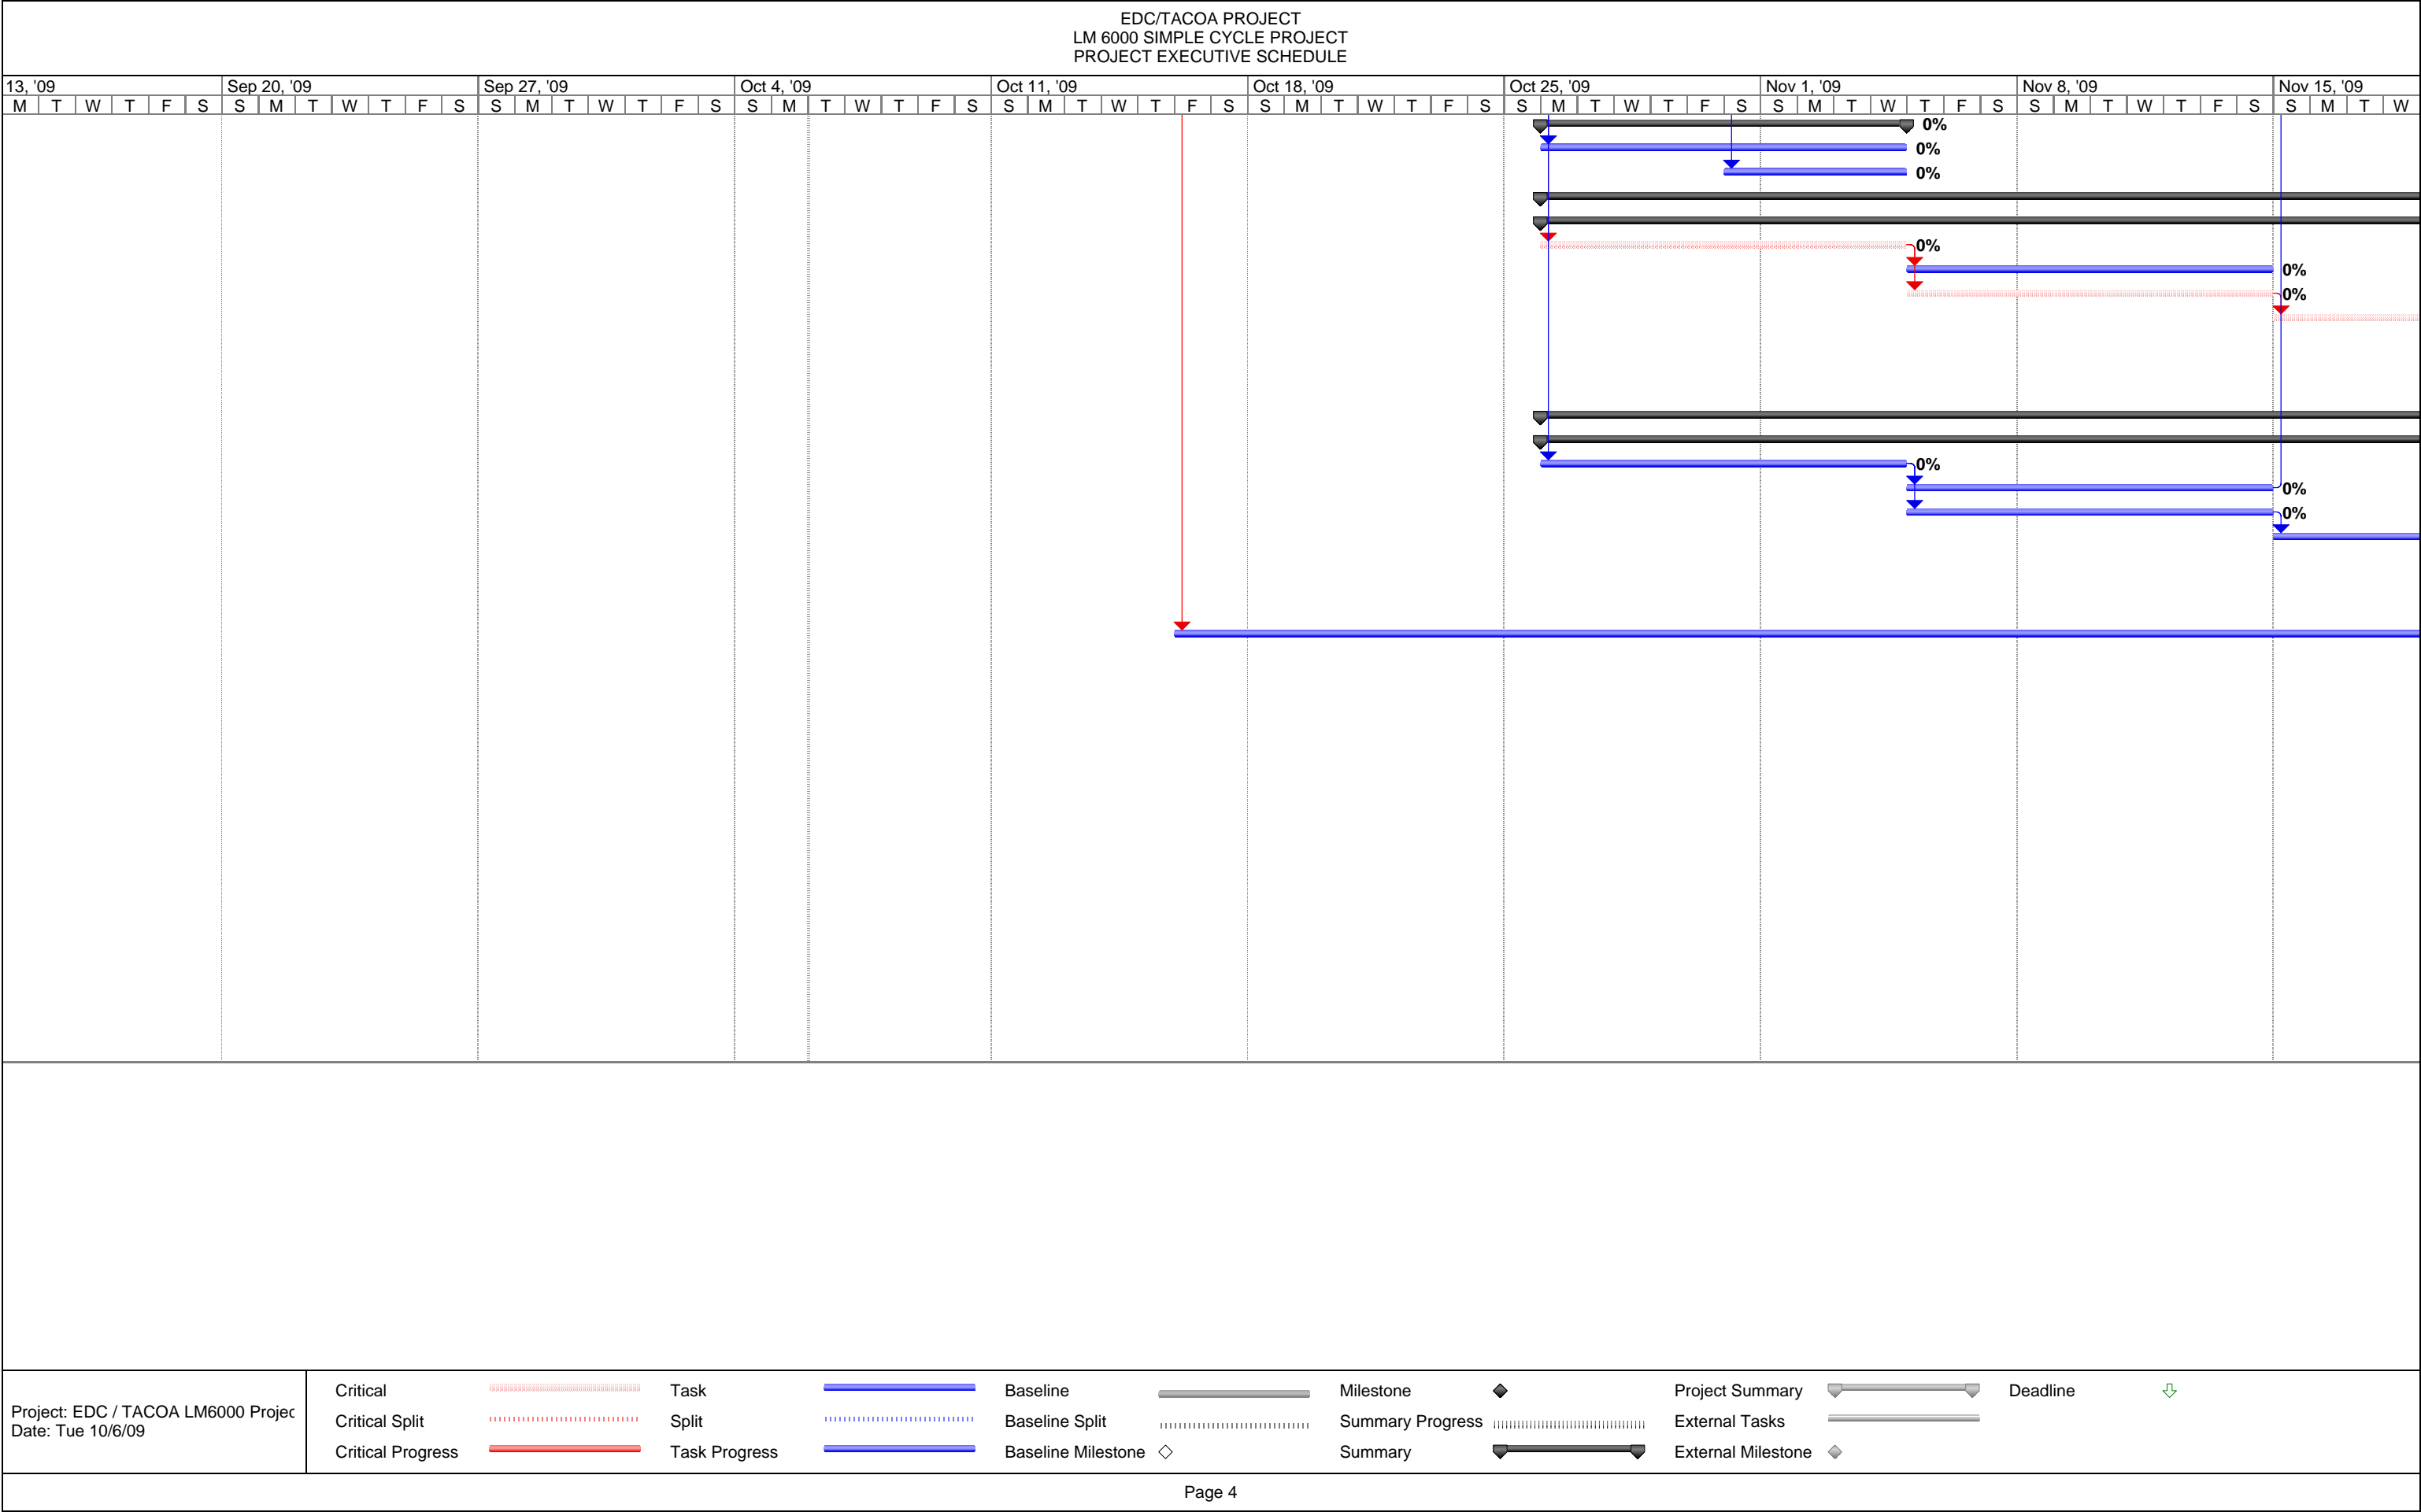

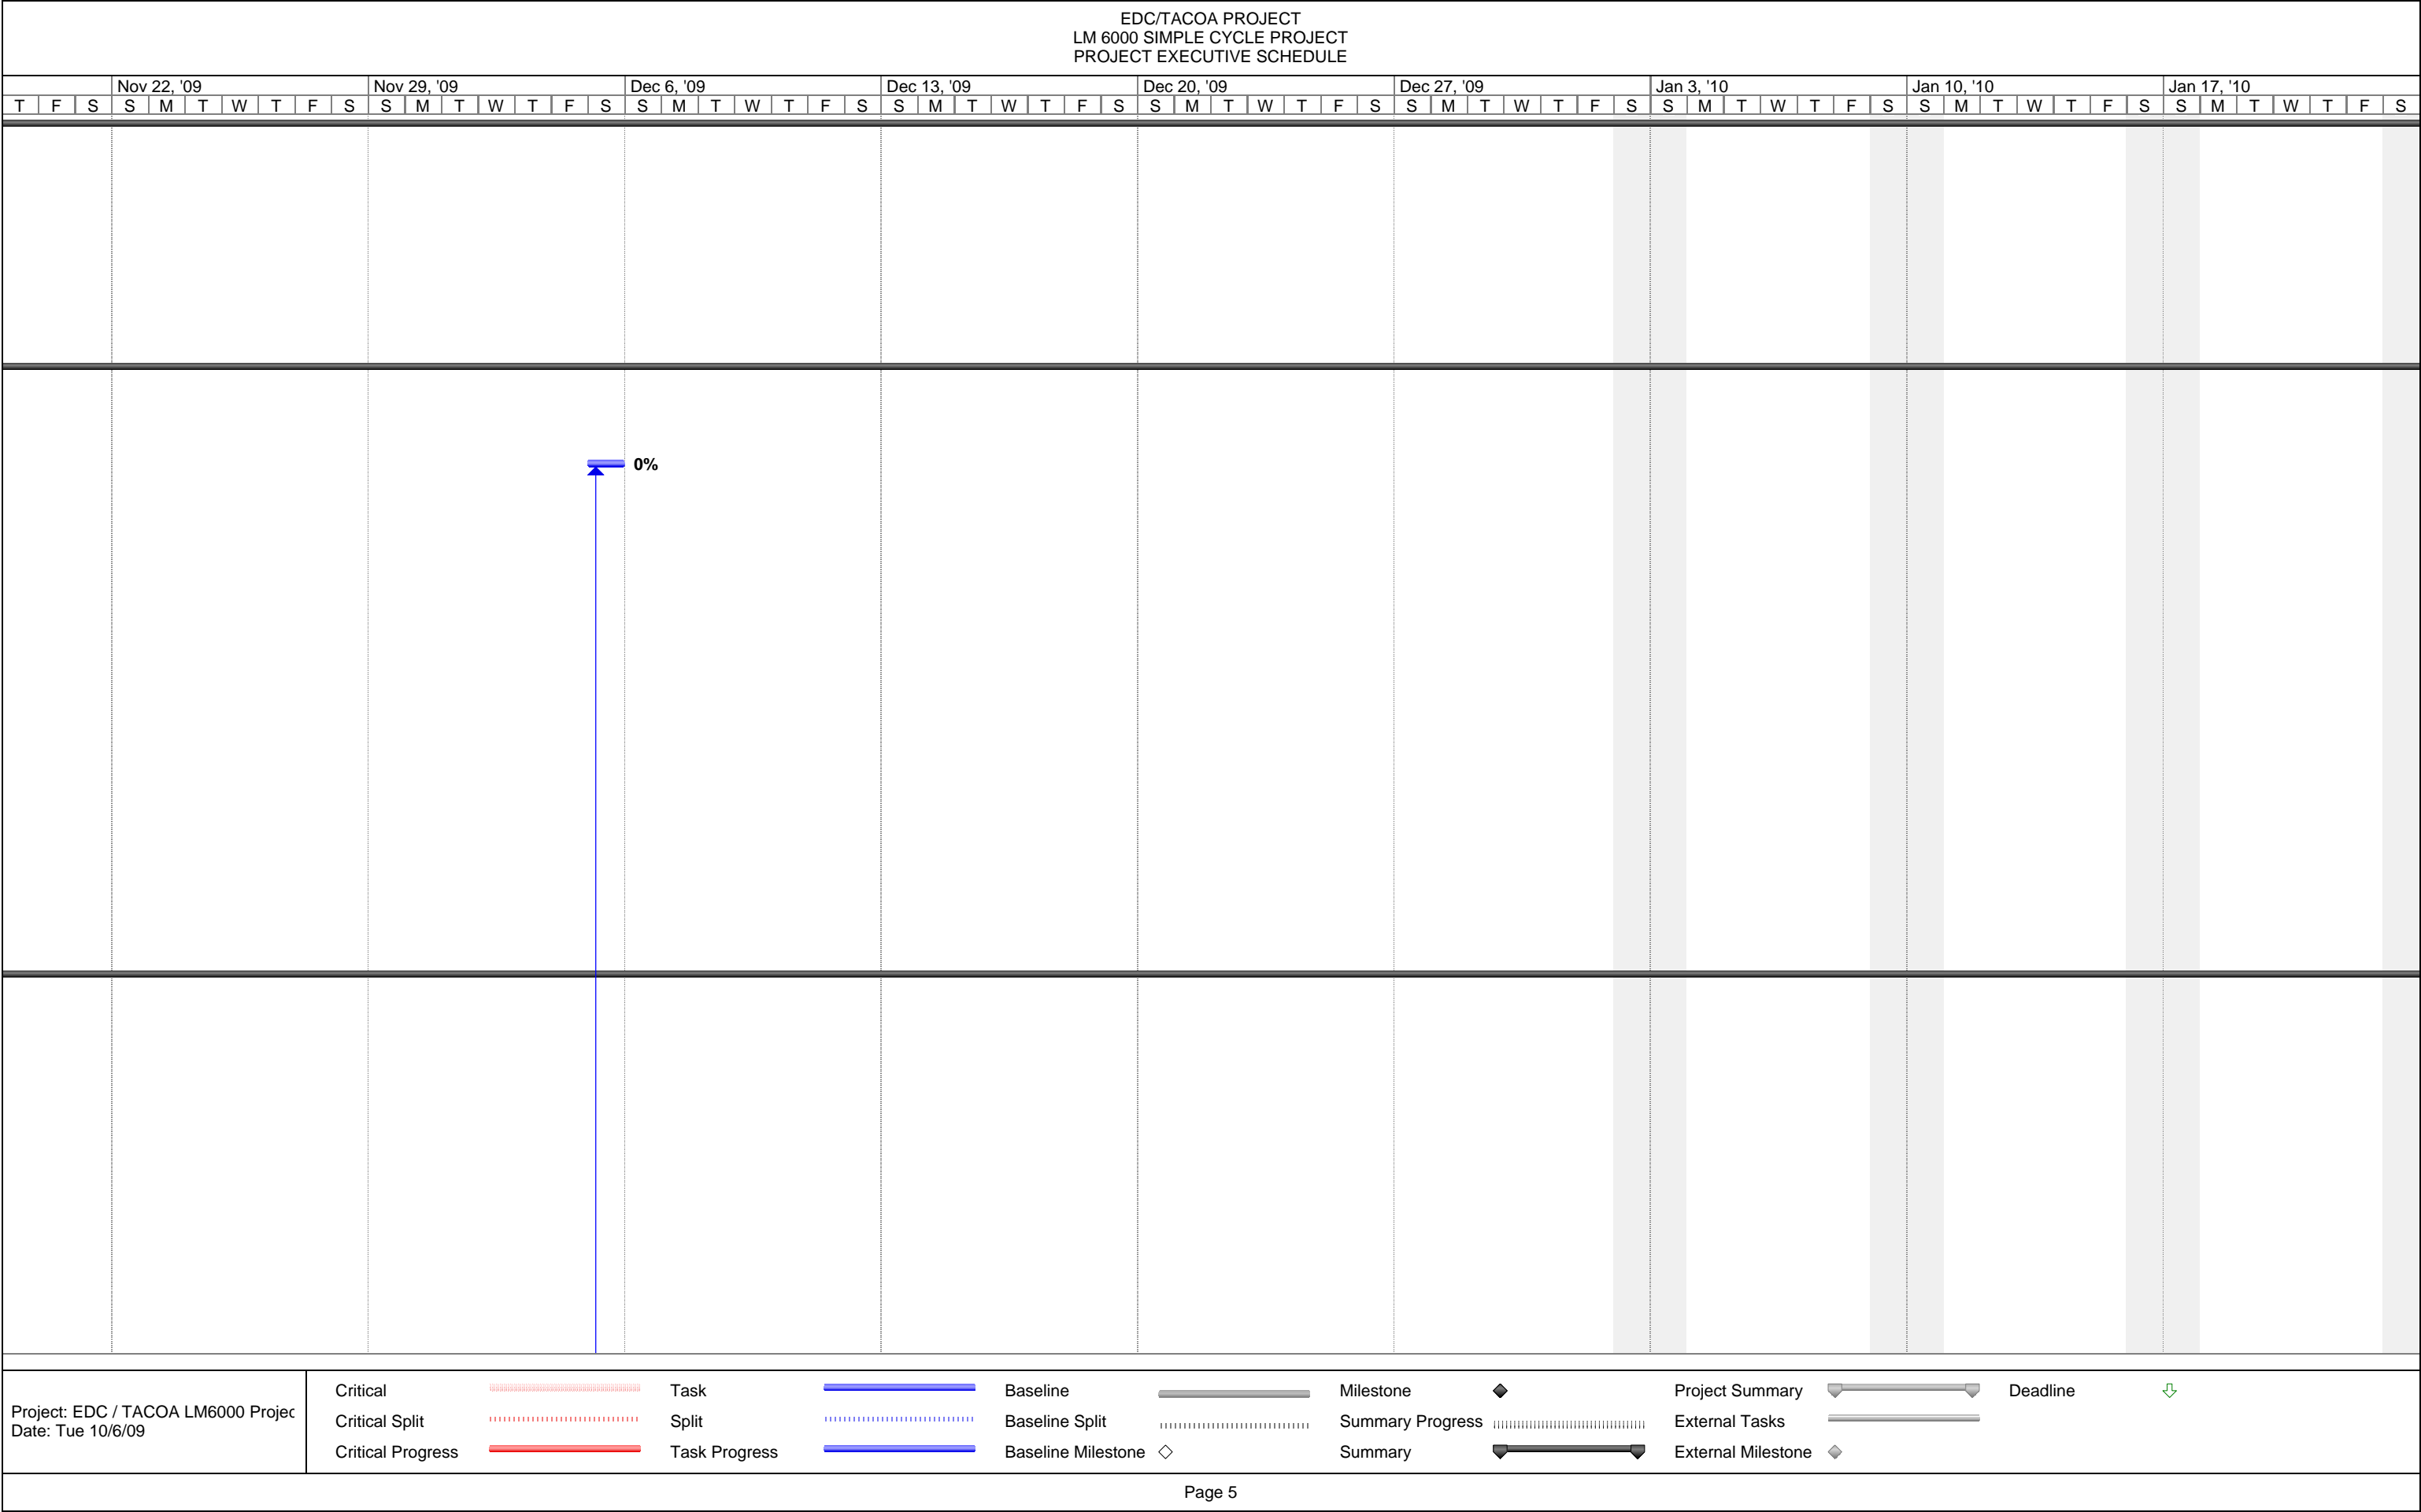

EDC/TACO PROJECT
LM 6000 SIMPLE CYCLE PROJECT
PROJECT EXECUTIVE SCHEDULE

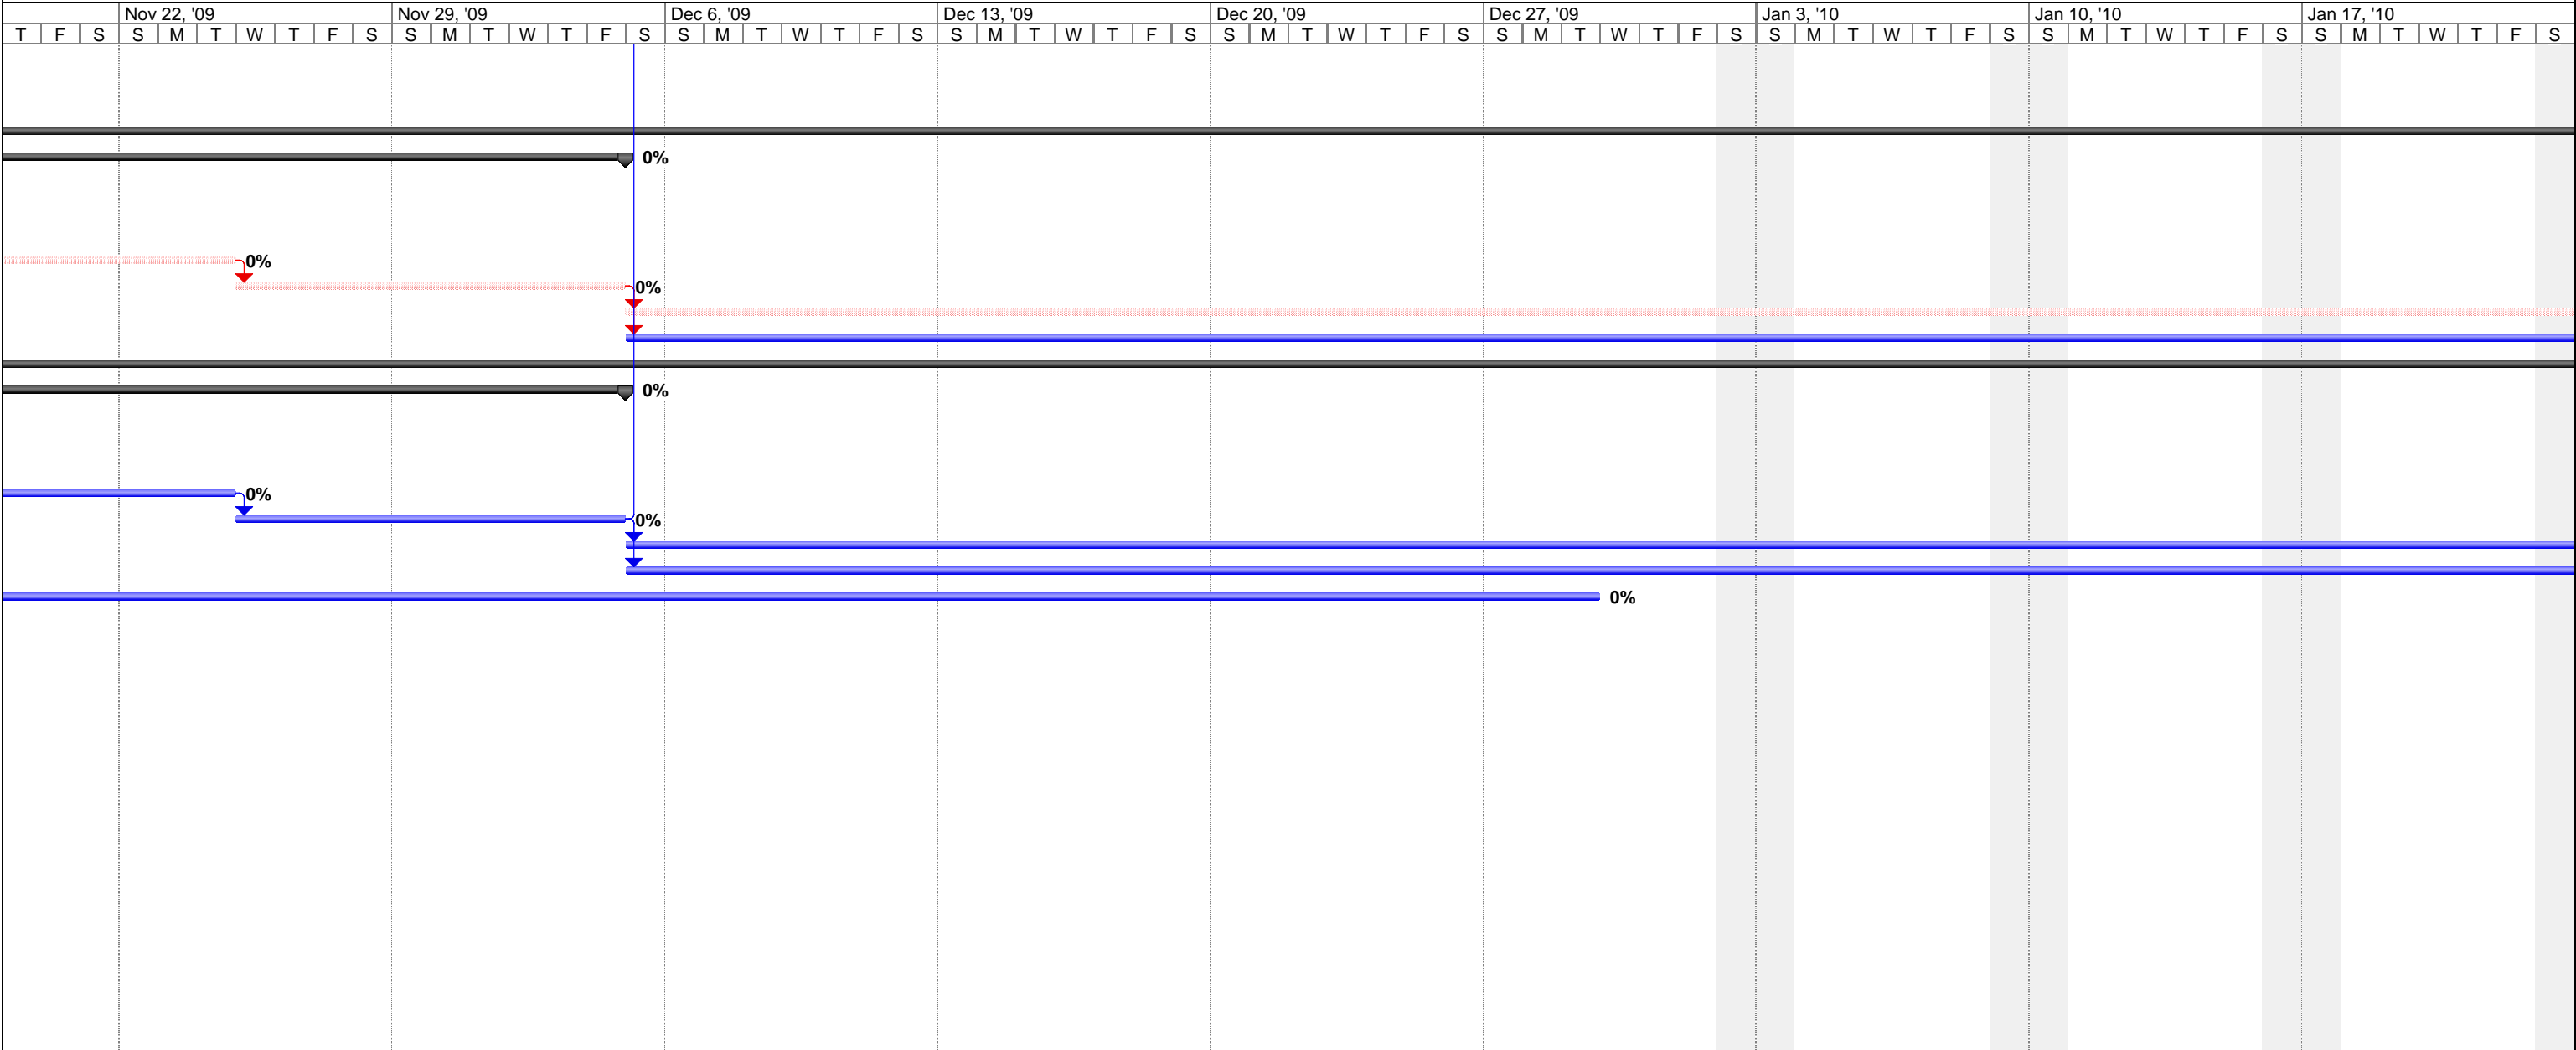


Project: EDC / TACOA LM6000 Project
Date: Tue 10/6/09


[illegible][illegible]

.....

8

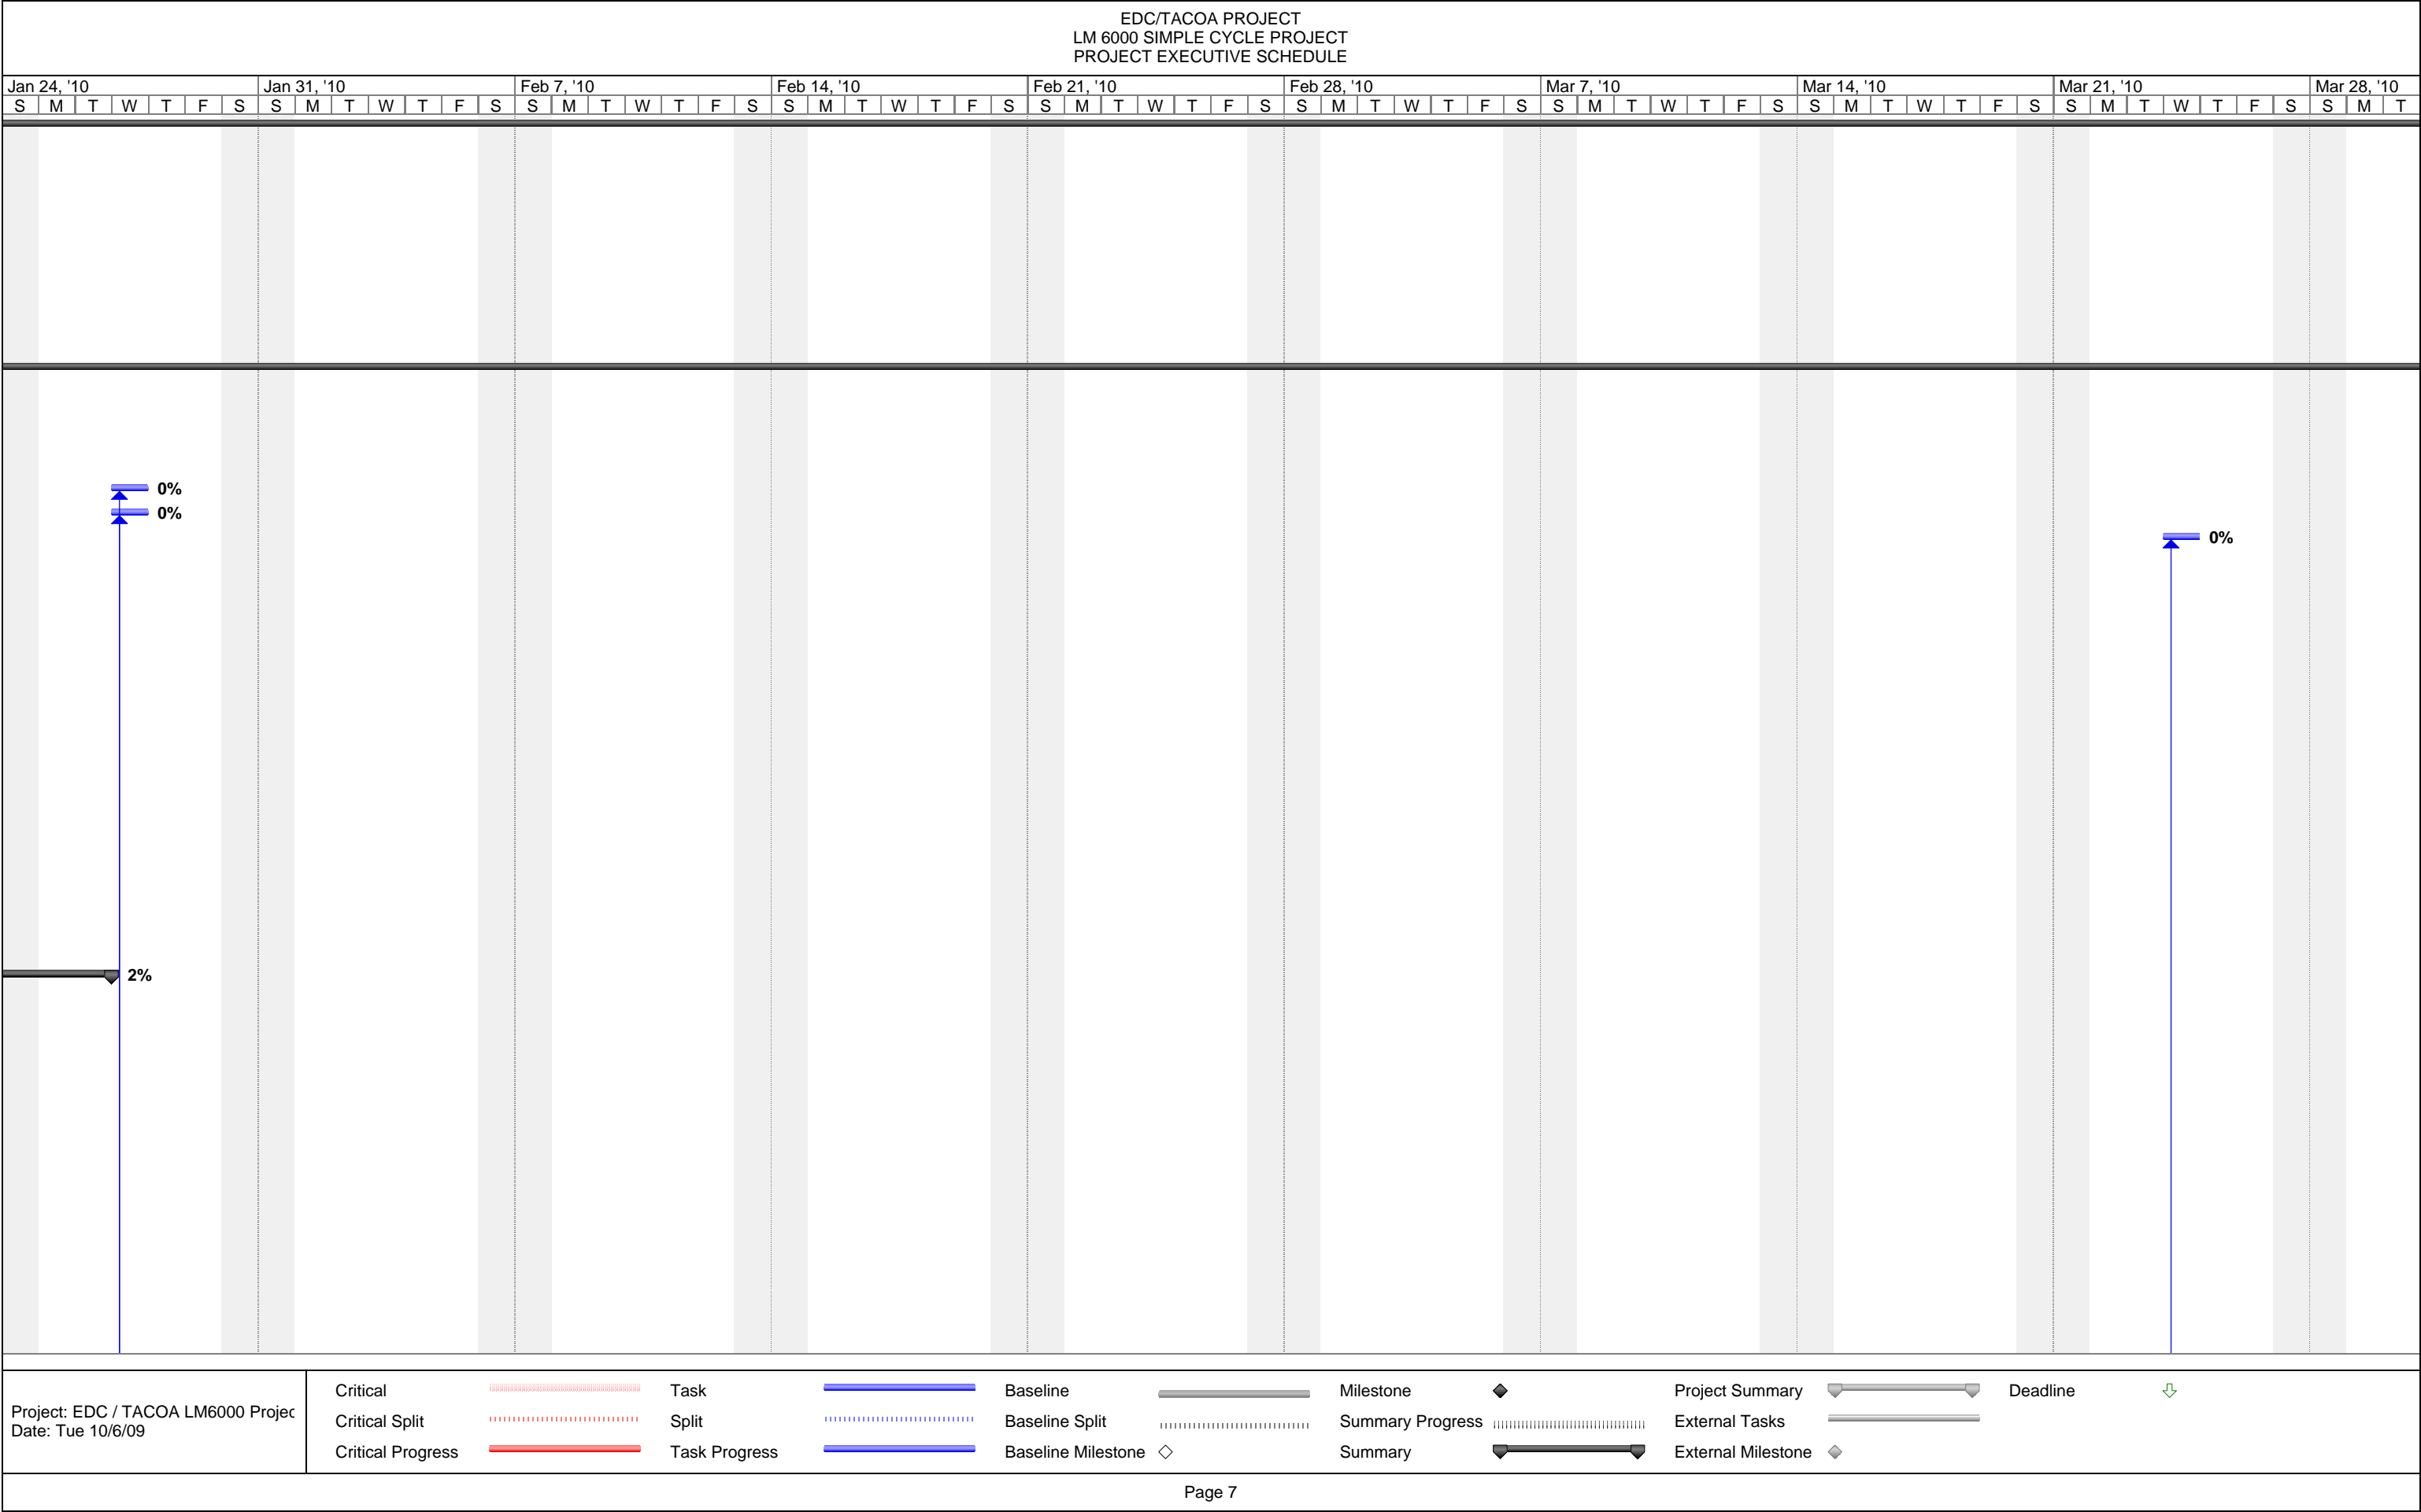


EDC/TACOA PROJECT
LM 6000 SIMPLE CYCLE PROJECT
PROJECT EXECUTIVE SCHEDULE

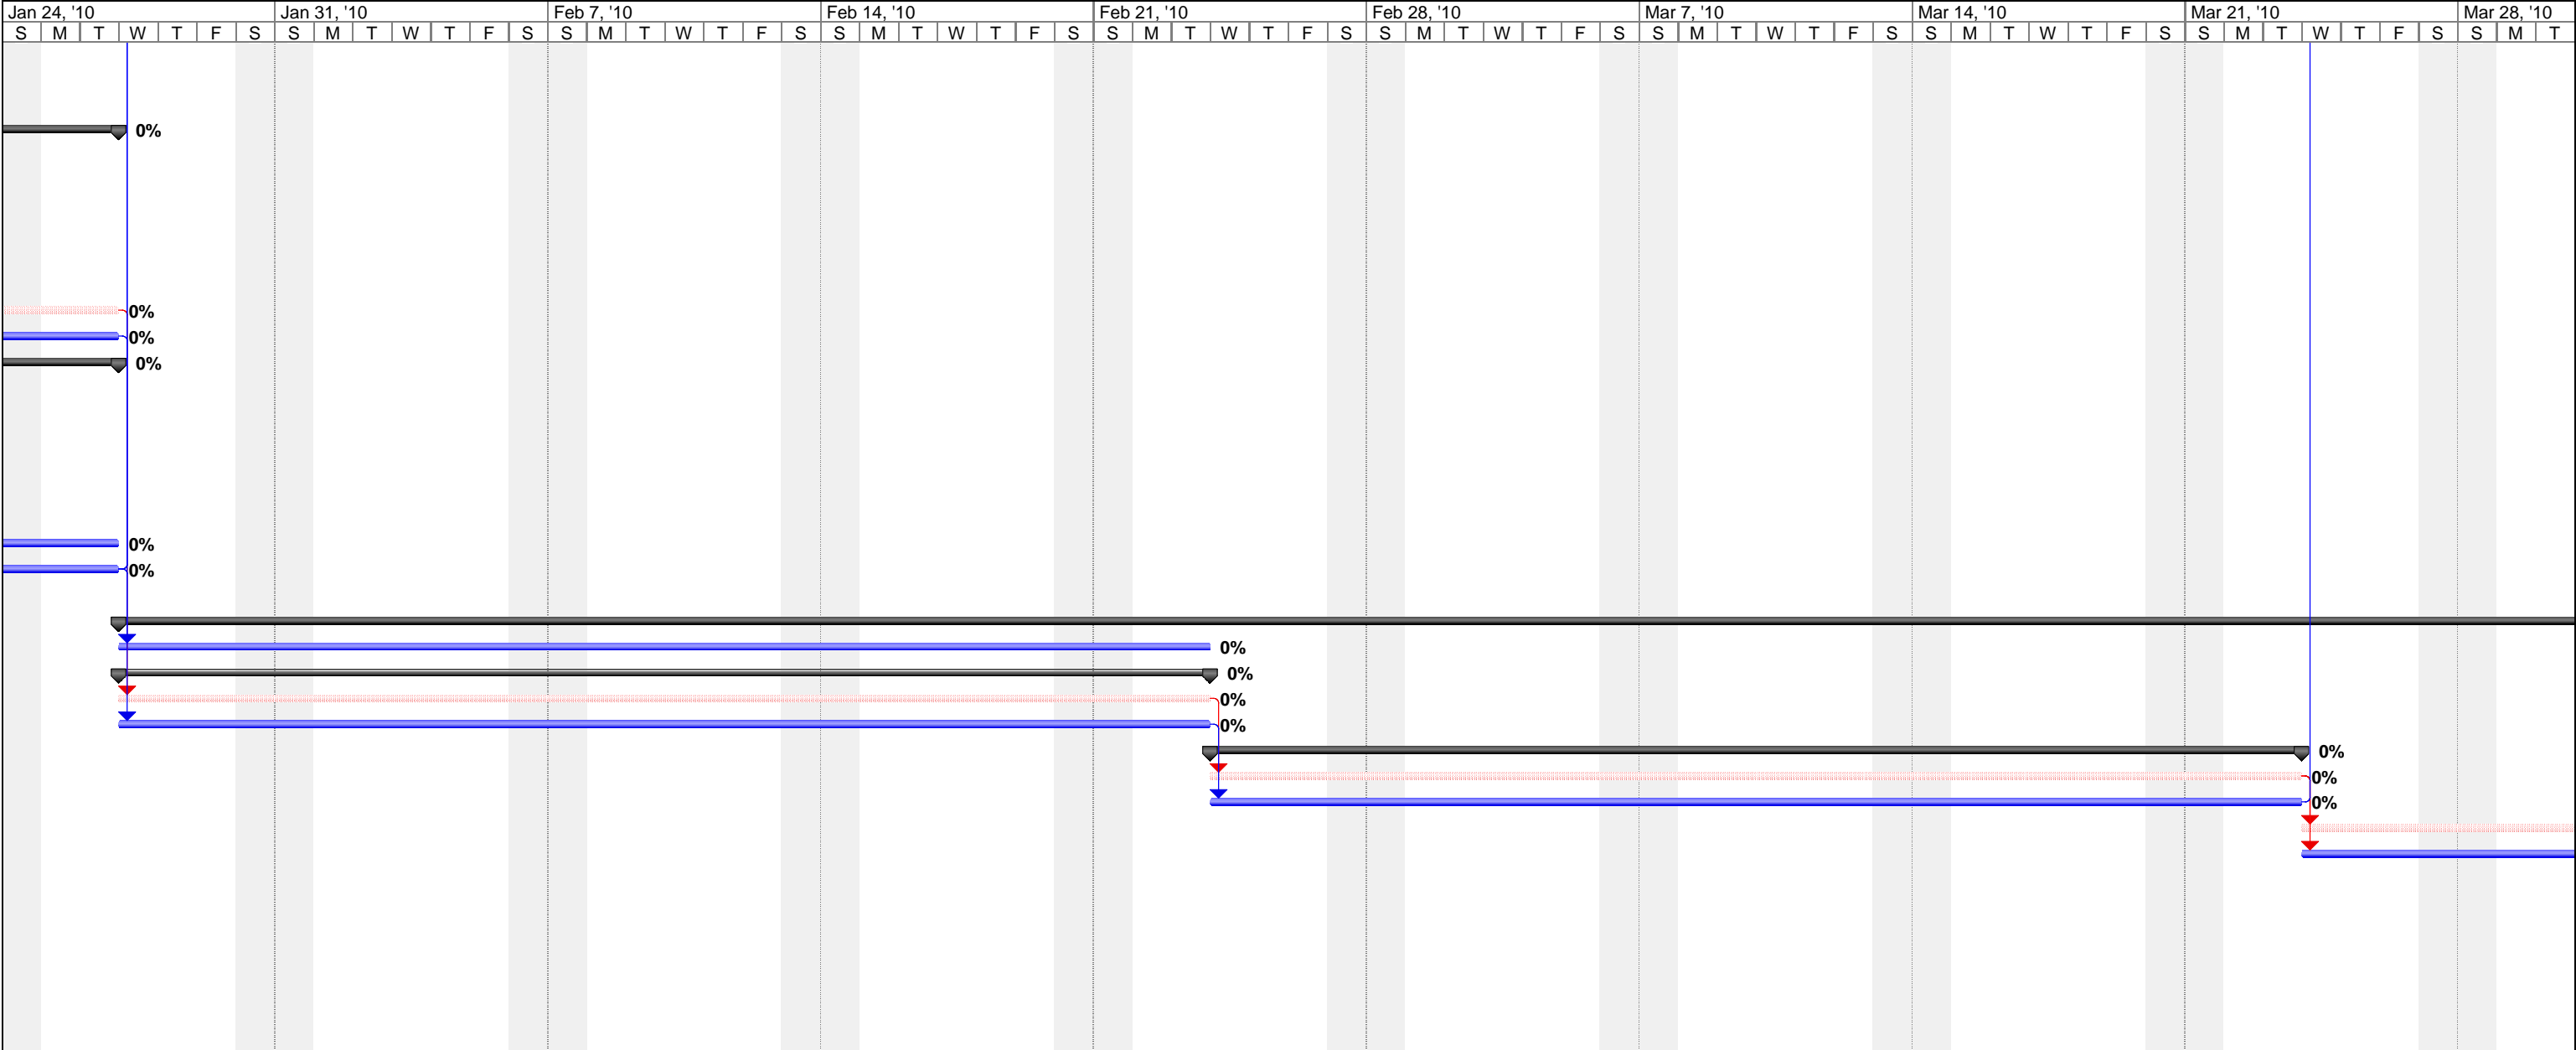


Project: EDC / TACOA LM6000 Projec Date: Tue 10/6/09	Critical		Task		Baseline		Milestone		Project Summary		Deadline	
	Critical Split		Split		Baseline Split		Summary Progress		External Tasks			
	Critical Progress		Task Progress		Baseline Milestone		Summary		External Milestone			

EDC/TACO PROJECT
LM 6000 SIMPLE CYCLE PROJECT
PROJECT EXECUTIVE SCHEDULE

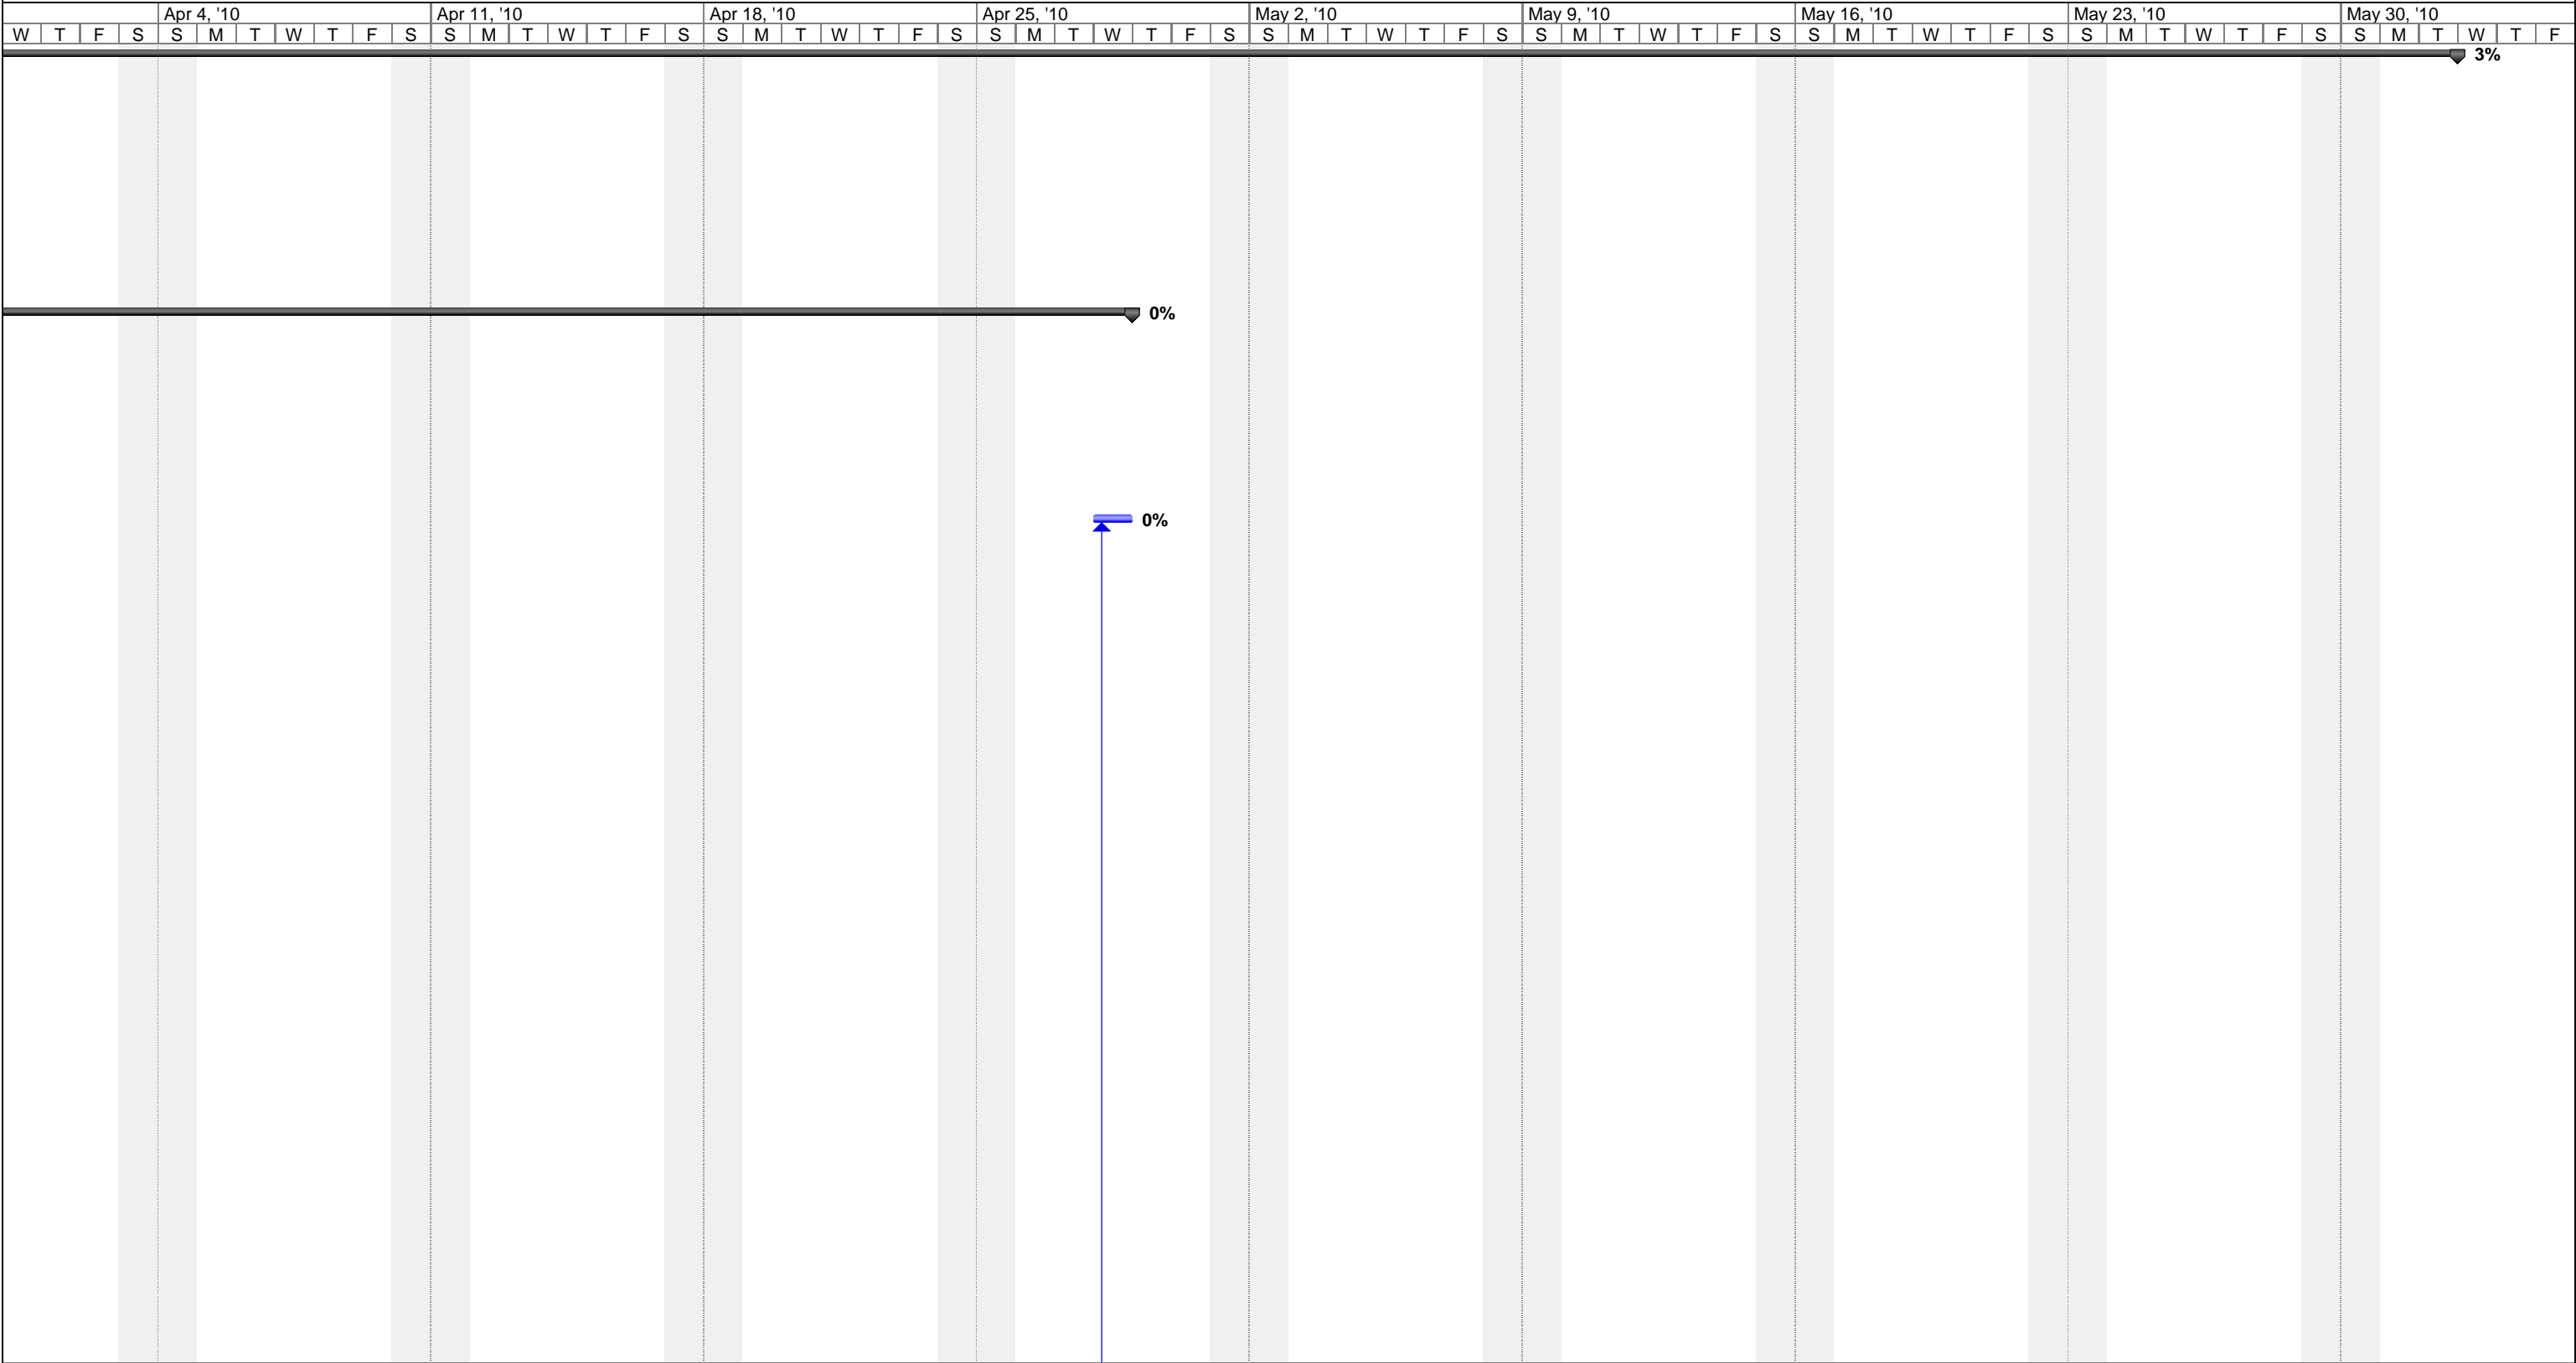

Project: EDC / TACOALM6000 Project Date: Tue 10/6/09	Critical Task Baseline Milestone Project Summary Deadline
	Critical Split Split Baseline Split Summary Progress External Tasks
	Critical Progress Task Progress Baseline Milestone Summary External Milestone

EDC/TACOA PROJECT
LM 6000 SIMPLE CYCLE PROJECT
PROJECT EXECUTIVE SCHEDULE

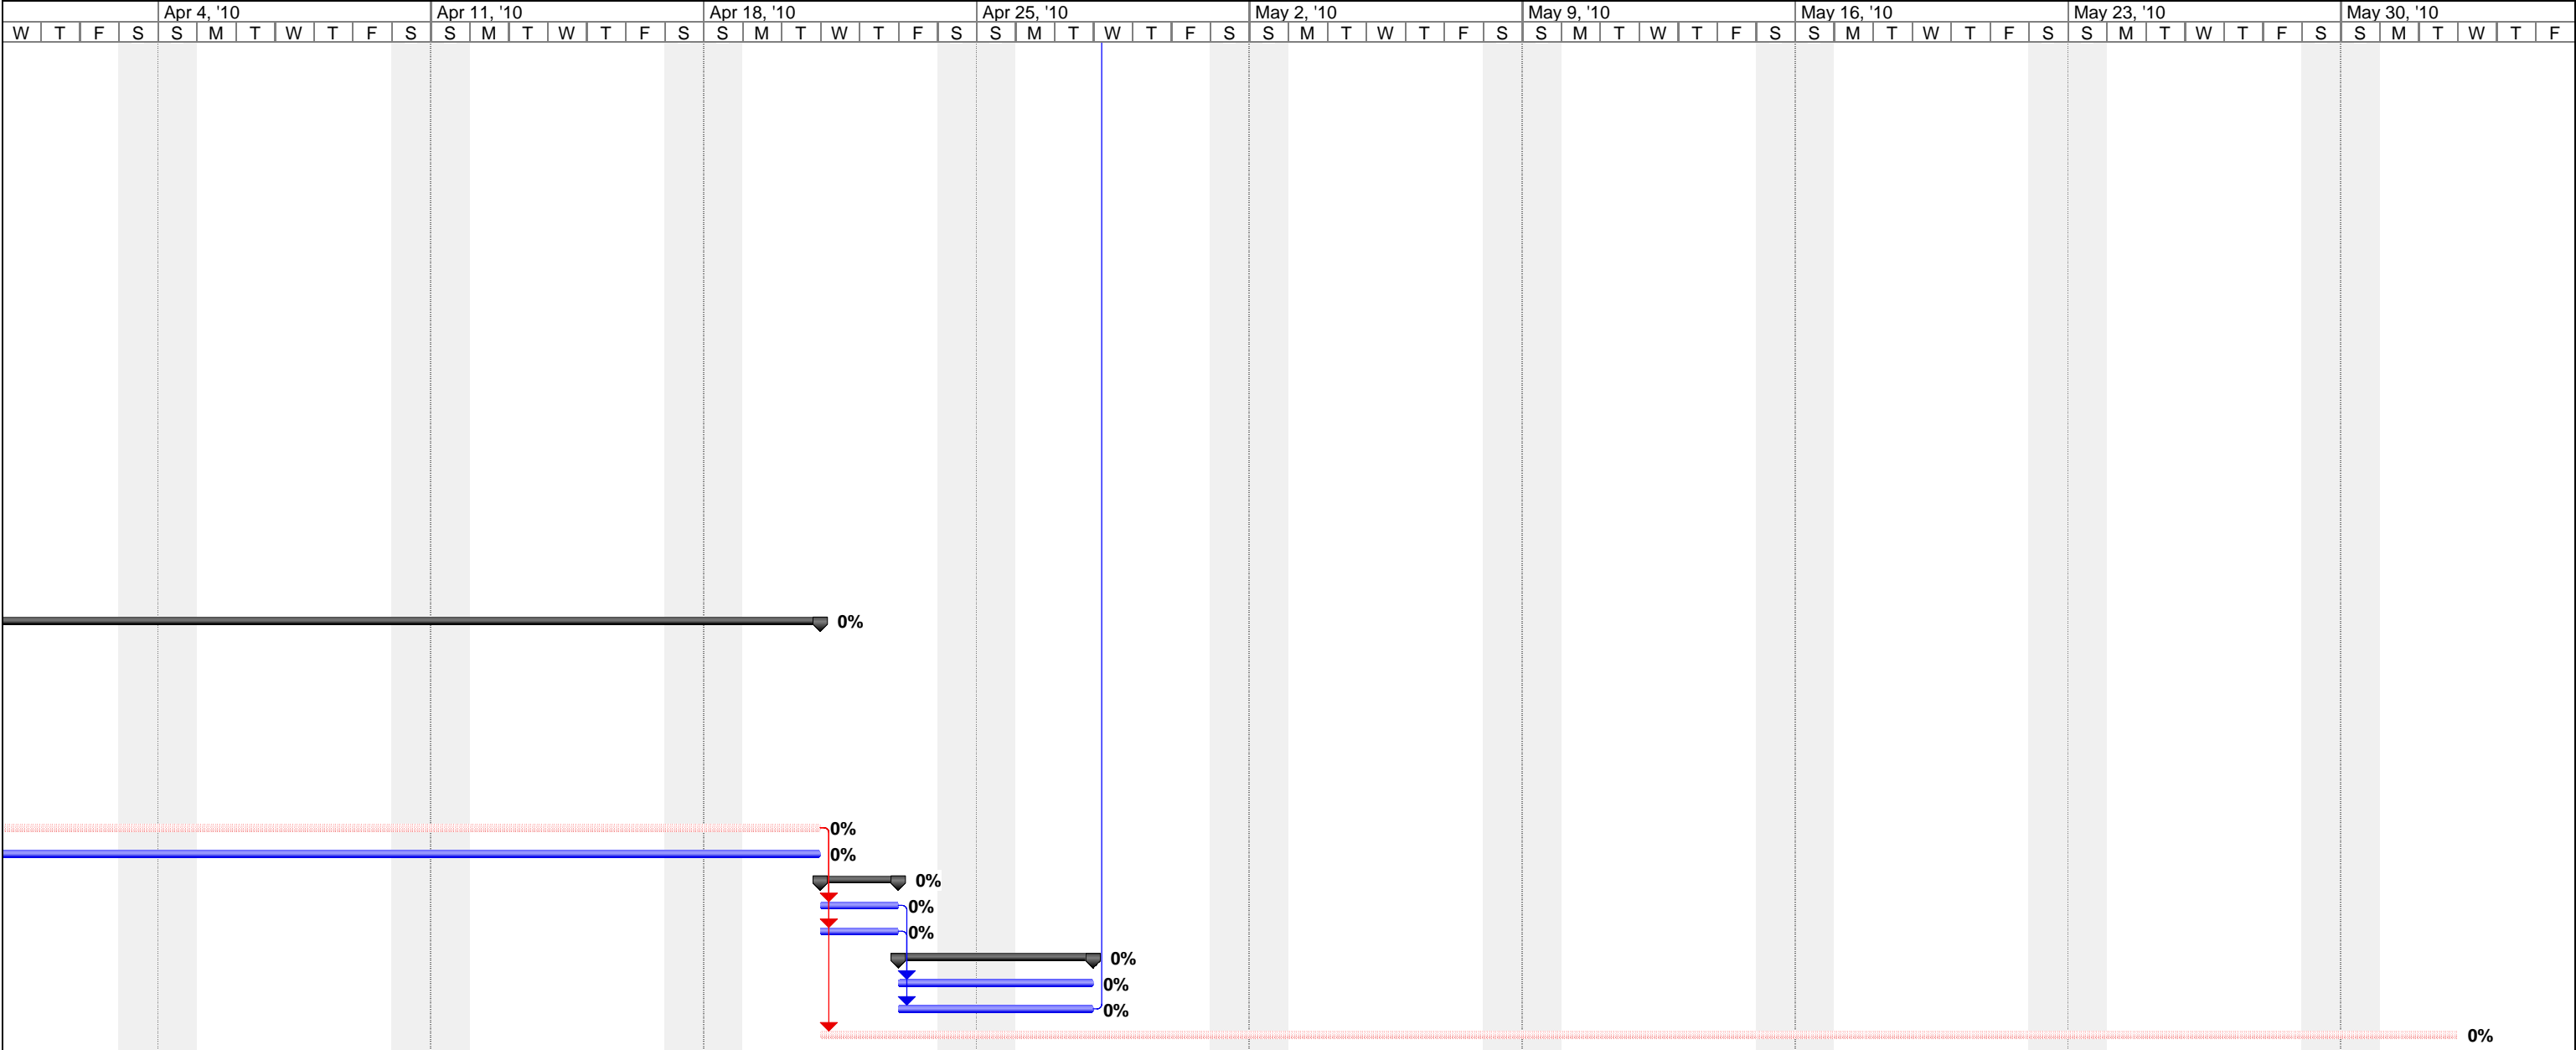

Project: EDC / TACOA LM6000 Projec
Date: Tue 10/6/09

Critical

Critical Split

Critical Progress

Task

Split

Task Progress

Baseline

Baseline Split

Baseline Milestone

Milestone

Summary Progress

Summary

Project Summary

External Tasks

External Milestone

Deadline
