


EDC Project  
LM2500 Simple Cycle Project  
Project Executive Schedule



Project: EDC LM2500 Project Executiv  
Date: Thu 1/29/09

Task

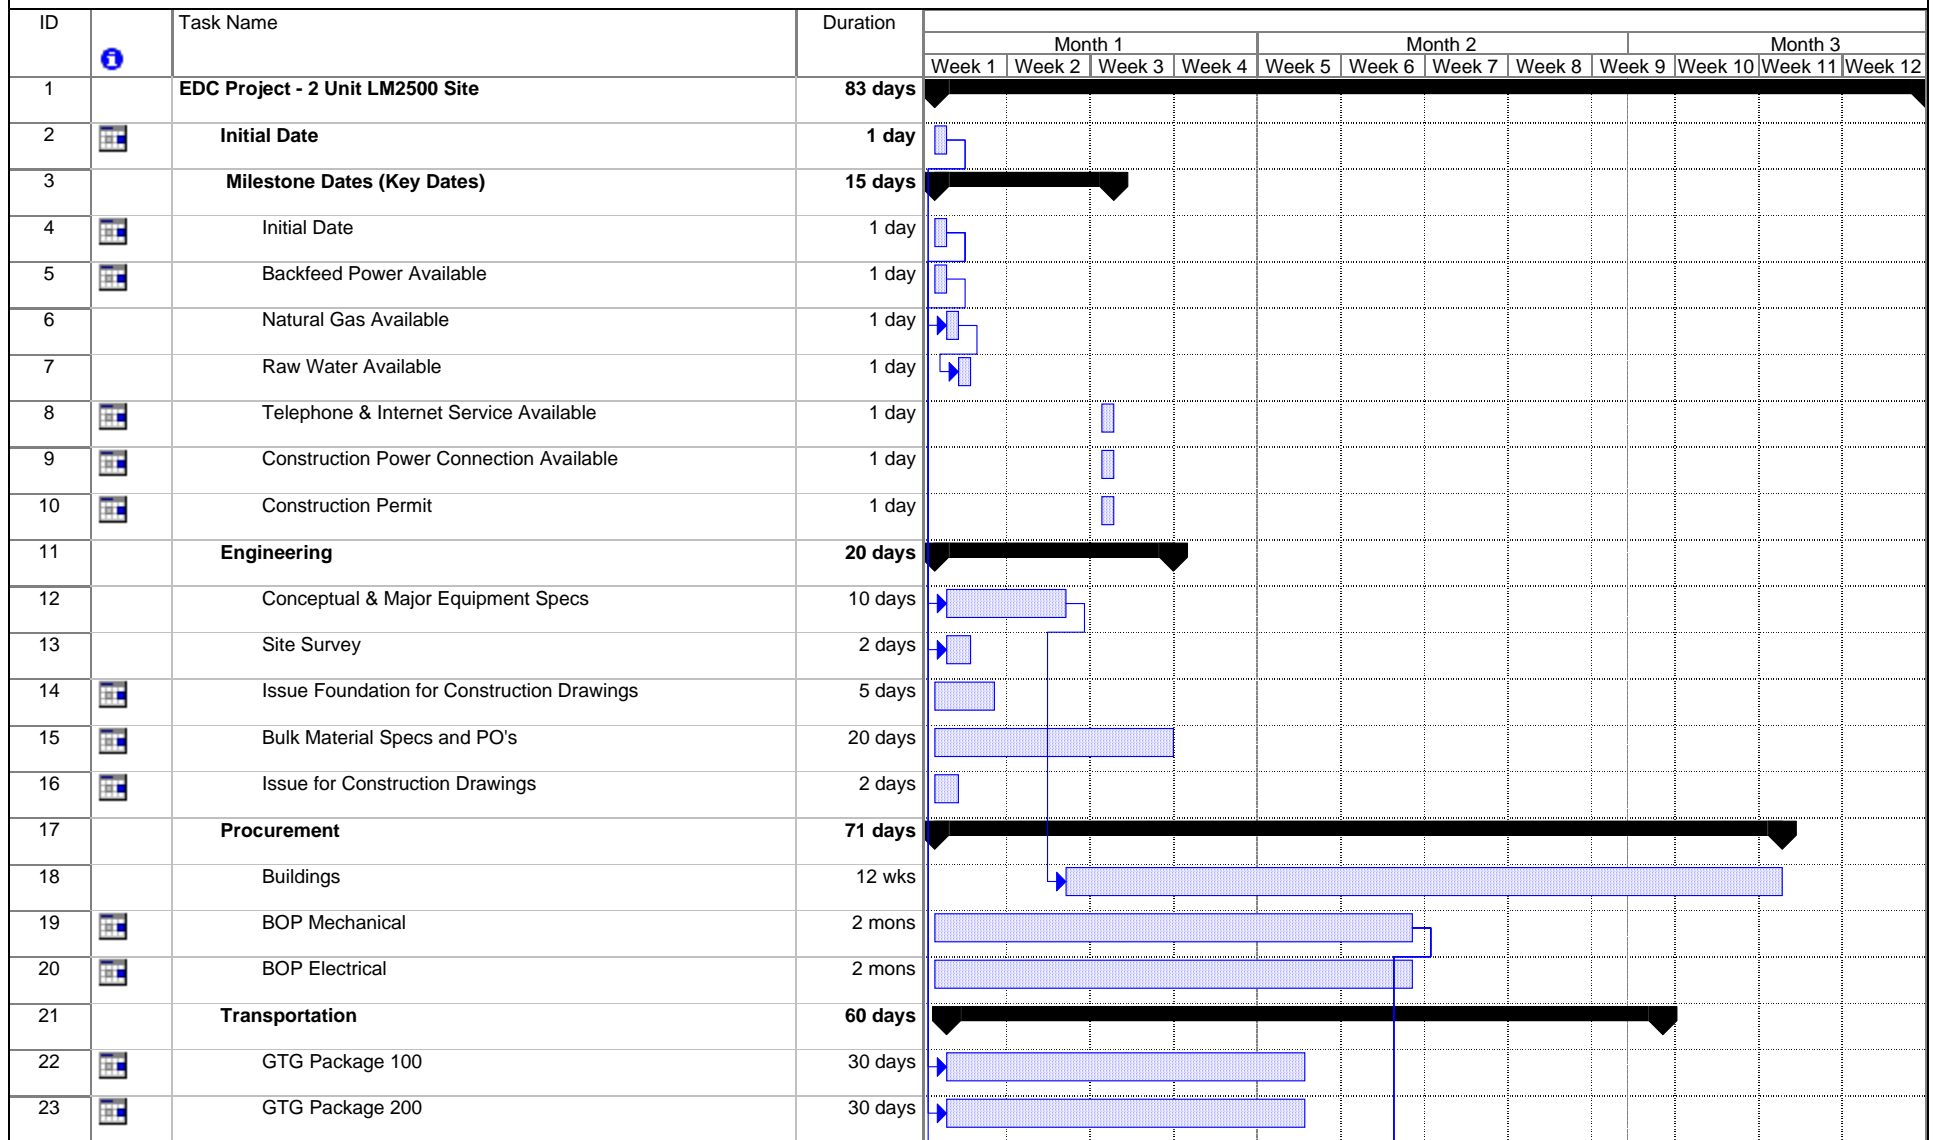


Milestone



External Tasks



Split



Summary



External Milestone



Progress

































Project Summary



Deadline



EDC Project  
LM2500 Simple Cycle Project  
Project Executive Schedule

ID		Task Name	Duration	Month 1												Month 2				Month 3			
				Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12	Week 1	Week 2	Week 3	Week 4	Week 1	Week 2	Week 3	Week 4
24		GSU's	60 days																				
25		<b>Construction</b>	<b>69 days</b>																				
26		<b>Mobilize to Site</b>	<b>14 days</b>																				
27		<b>Civil Work</b>	<b>42 days</b>																				
28		Site Preparation	10 days																				
29		Excavation & Grading	15 days																				
30		Install Perimeter Fence	12 days																				
31		<b>Power Island Foundations</b>	<b>10 days</b>																				
32		GTG 100	5 days																				
33		GTG 200	5 days																				
34		GSU 100	4 days																				
35		GSU 200	5 days																				
36		<b>BOP Foundations</b>	<b>25 days</b>																				
37		Unit Building	10 days																				
38		Substation	10 days																				
39		Substation Bldg	5 days																				
40		Pipe Racks	5 days																				
41		<b>Building Erection &amp; Fit-out</b>	<b>10 days</b>																				
42		Unit Building	10 days																				
43		Erect Substation Bldg	5 days																				
44		<b>Erect GTG 100</b>	<b>19 days</b>																				
45		<b>Equipment Erection</b>	<b>9 days</b>																				
46		Generator	1 day																				

Project: EDC LM2500 Project Executiv  
Date: Thu 1/29/09

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline



EDC Project  
LM2500 Simple Cycle Project  
Project Executive Schedule

ID		Task Name	Duration	Month 1												Month 2				Month 3			
				Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12	Week 1	Week 2	Week 3	Week 4	Week 1	Week 2	Week 3	Week 4
47		Gas Turbine	1 day																				
48		Air Inlet & Filter	2 days																				
49		GT Roof Panel Assy & Installation	3 days																				
50		GT Combustion Filter Assy & Installation	3 days																				
51		Electrical Installation	10 days																				
52		Mechanical Installation	10 days																				
53		<b>Erect GTG 200</b>	<b>19 days</b>																				
54		<b>Equipment Erection</b>	<b>9 days</b>																				
55		Generator	1 day																				
56		Gas Turbine	1 day																				
57		Air Inlet & Filter	2 days																				
58		GT Roof Panel Assy & Installation	3 days																				
59		GT Combustion Filter Assy & Installation	3 days																				
60		Electrical Installation	10 days																				
61		Mechanical Installation	10 days																				
62		<b>HV Installation</b>	<b>12 days</b>																				
63		Erect GSU's	12 days																				
64		<b>Install BOP Mechanical Eq.</b>	<b>27 days</b>																				
65		Install Oily Water Separator	5 days																				
66		Install Instrument Air Compressor	2 days																				
67		Install Fuel Gas Filter Skids	5 days																				
68		Install U/G Piping Header System	20 days																				
69		Install A/G Piping Header System	20 days																				

Project: EDC LM2500 Project Executiv  
Date: Thu 1/29/09

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress




Project Summary



Deadline



EDC Project  
LM2500 Simple Cycle Project  
Project Executive Schedule

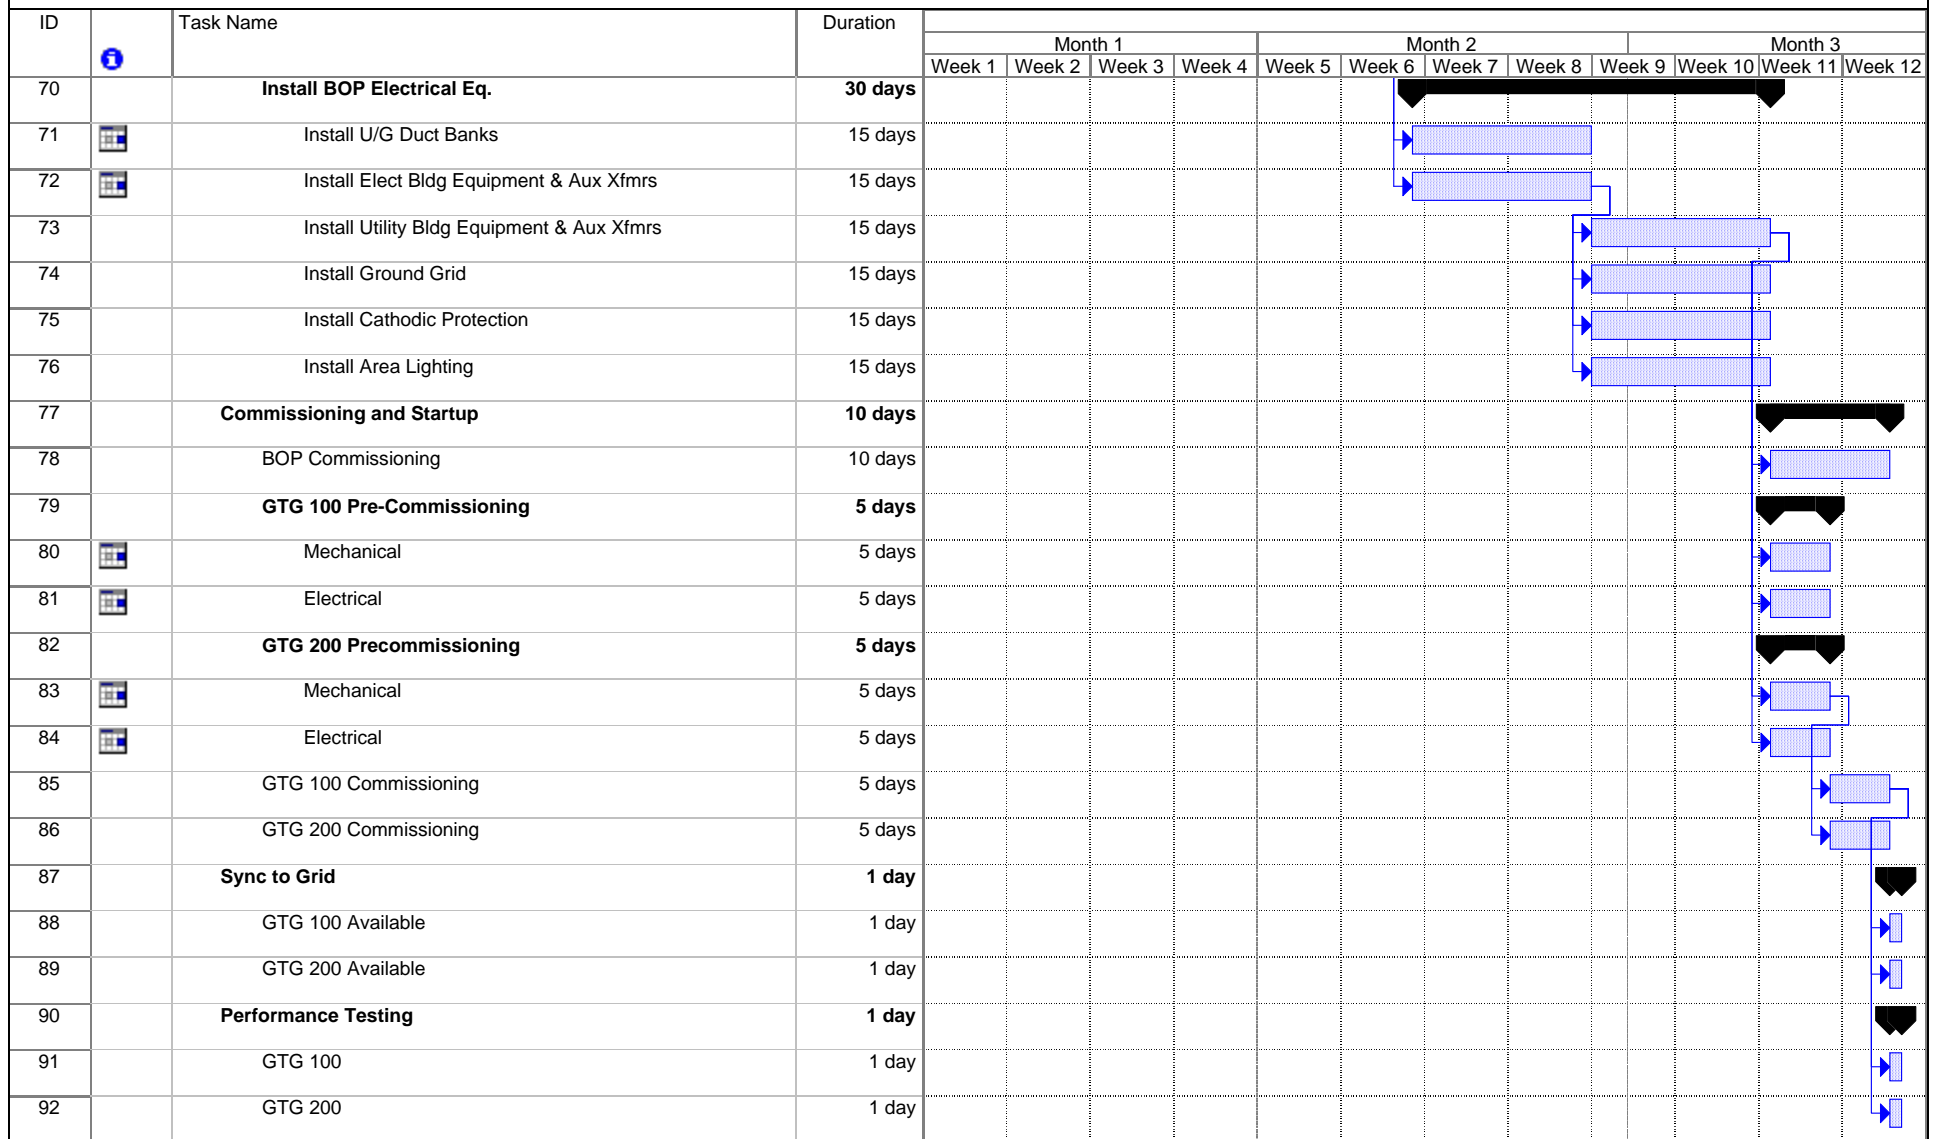

Project: EDC LM2500 Project Executiv  
Date: Thu 1/29/09

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline
