


EDC Project
LM6000 Simple Cycle Project
Project Executive Schedule



Project: EDC LM6000 Project Executiv
Date: Thu 1/29/09

Task

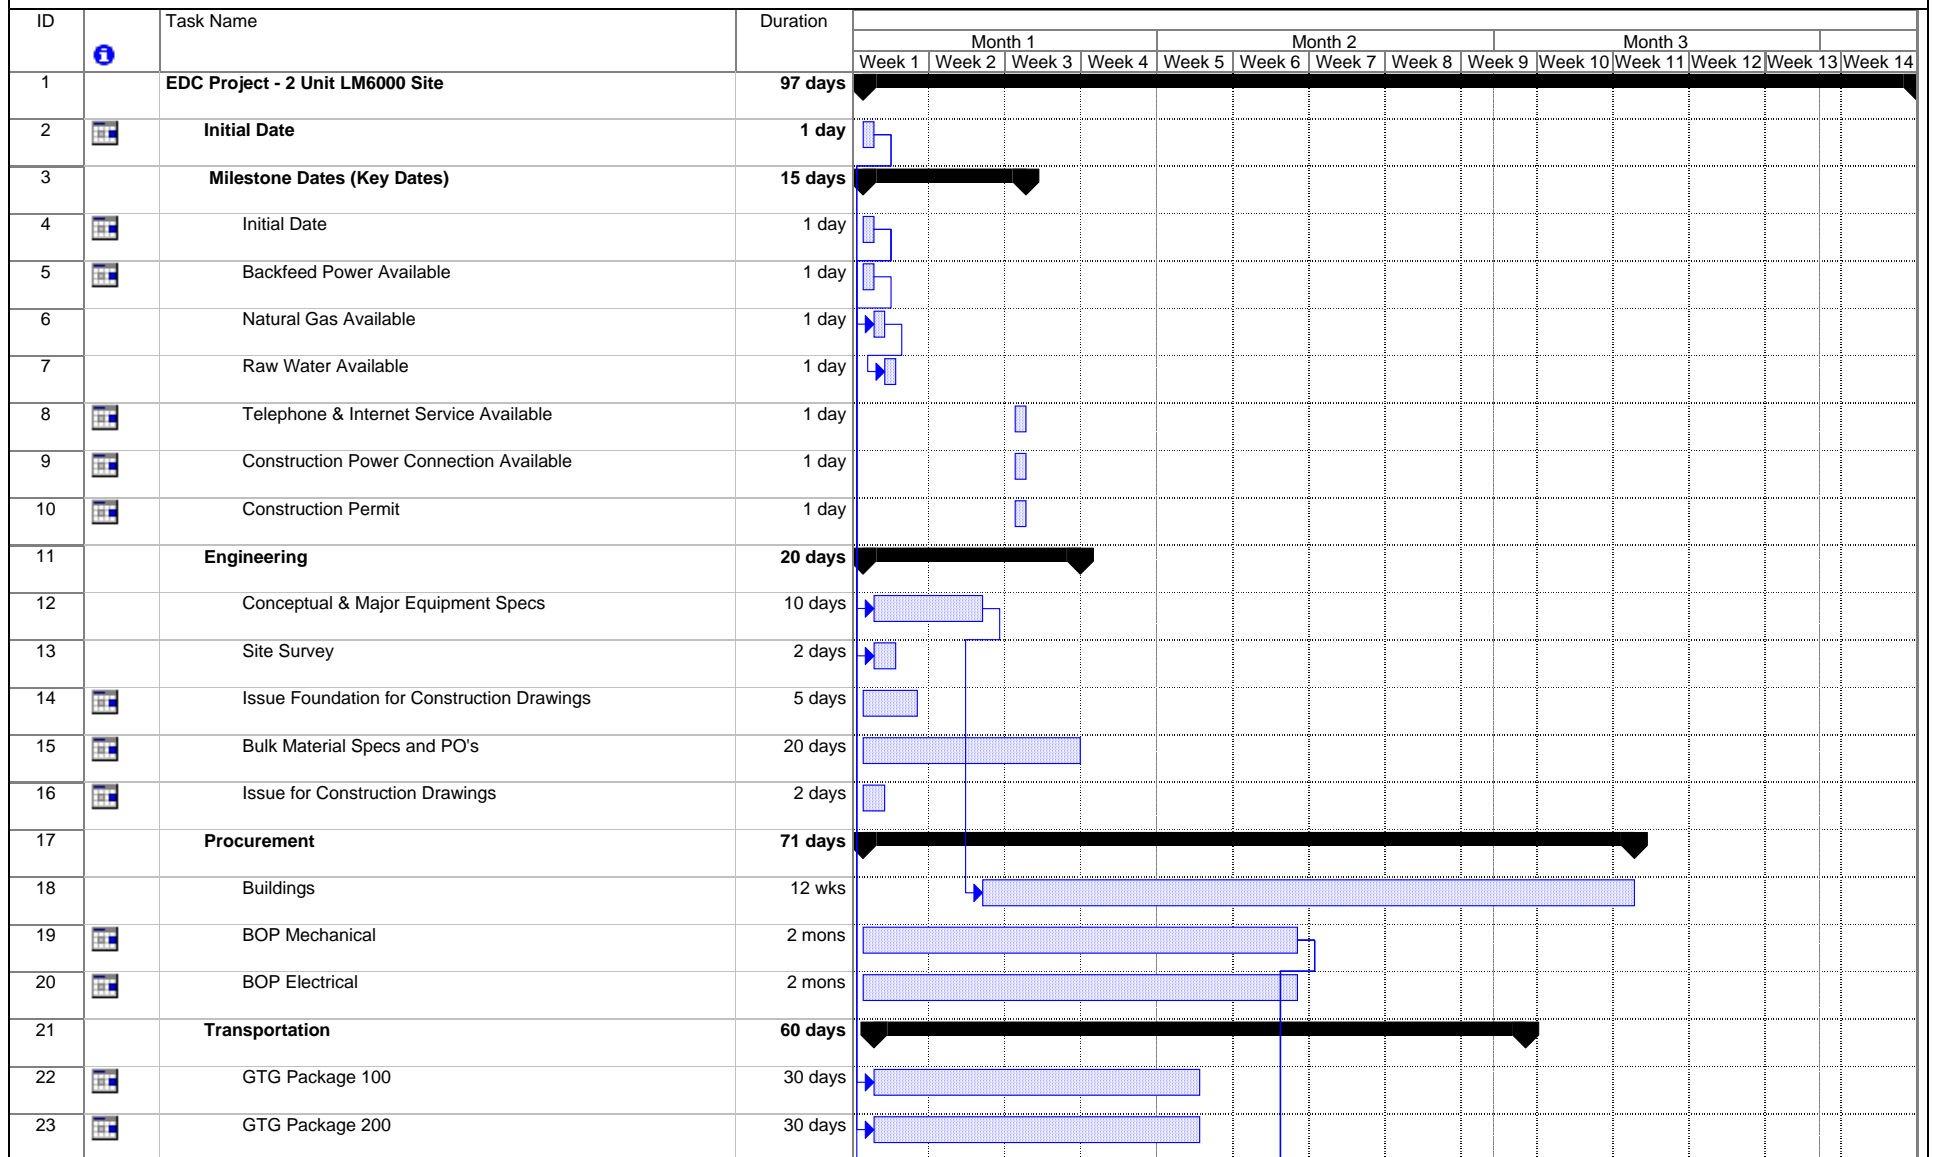

Milestone



External Tasks



Split



Summary



External Milestone



Progress




Project Summary



Deadline



EDC Project
LM6000 Simple Cycle Project
Project Executive Schedule

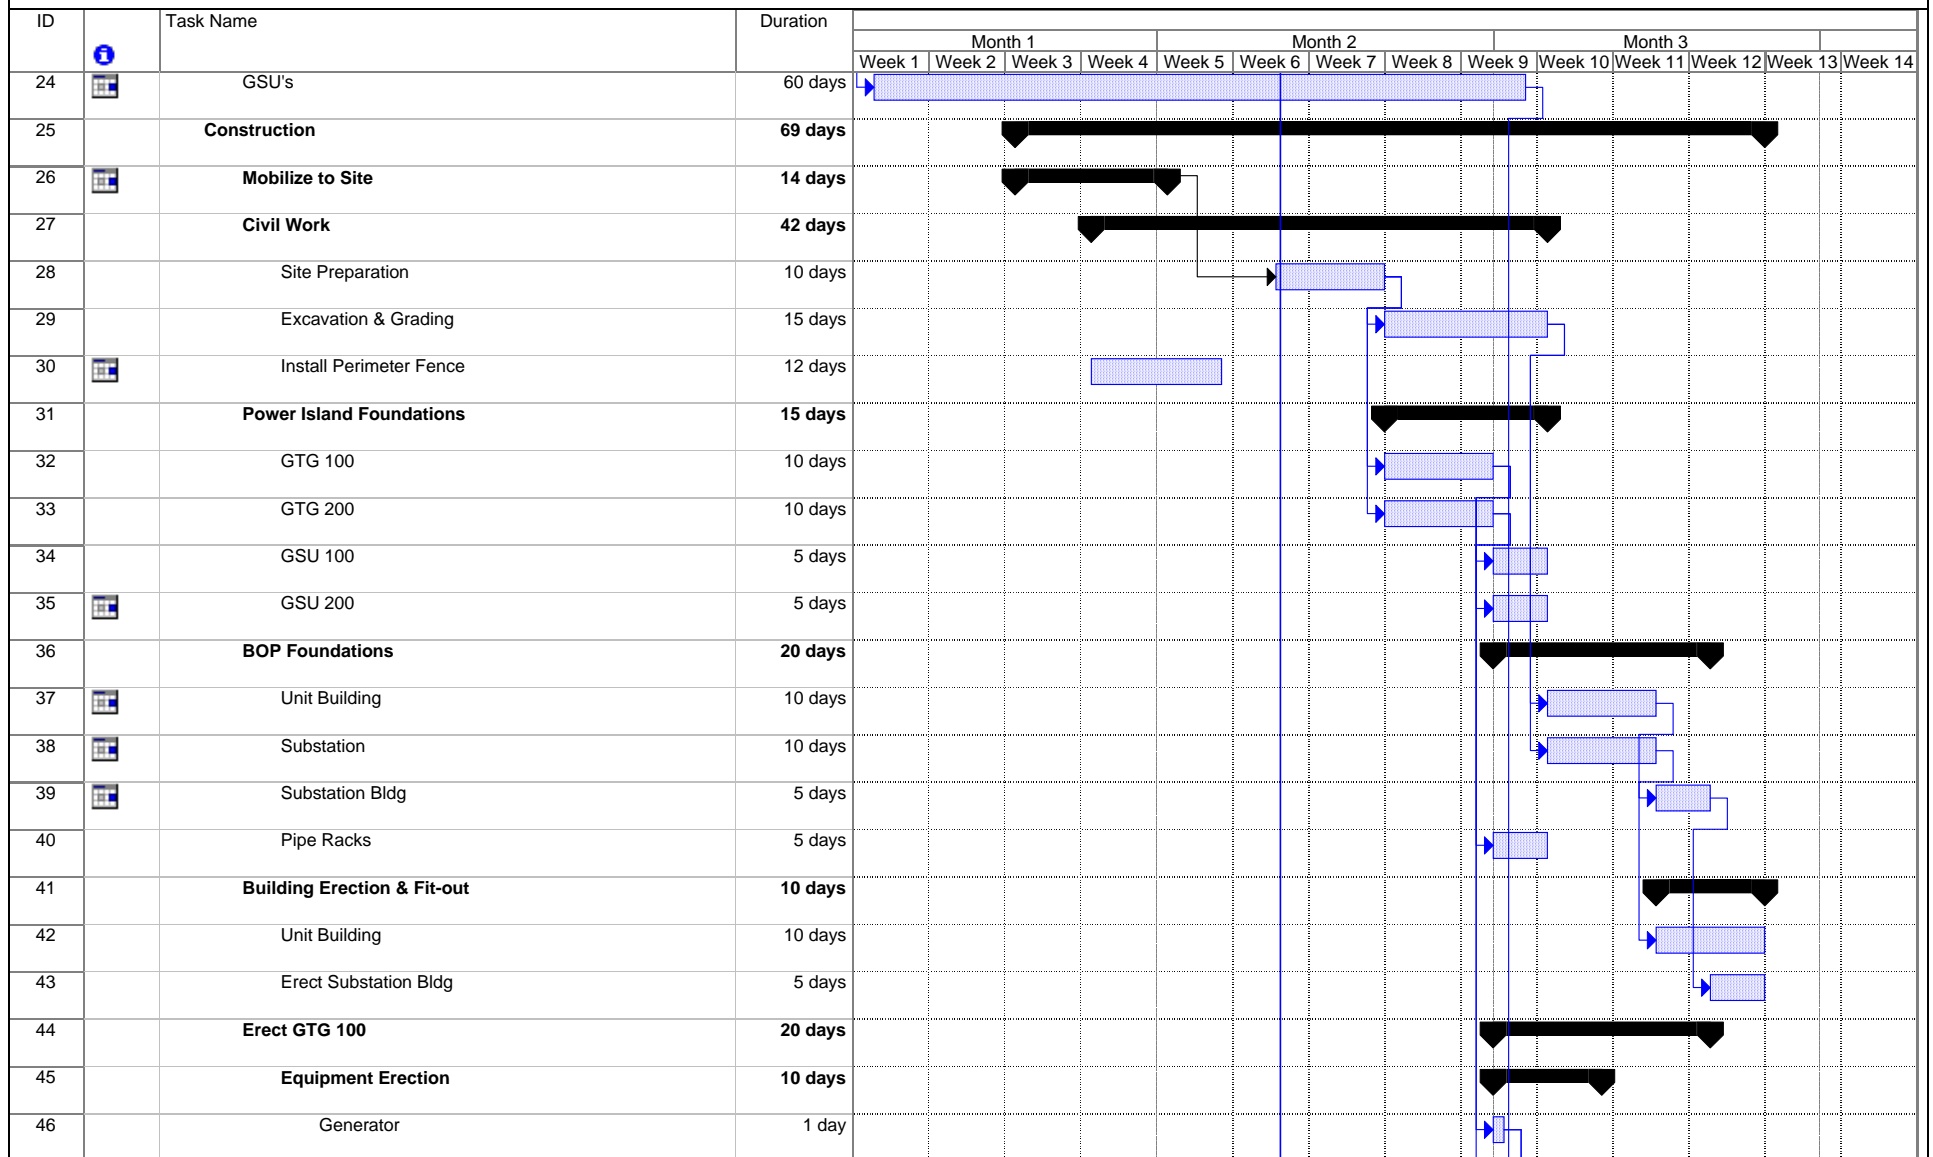

Project: EDC LM6000 Project Executiv
Date: Thu 1/29/09

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline



EDC Project LM6000 Simple Cycle Project Project Executive Schedule																
ID		Task Name	Duration	Month 1				Month 2				Month 3				
				Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12	
47		Gas Turbine	1 day													
48		Air Inlet & Filter	3 days													
49		GT Roof Panel Assy & Installation	3 days													
50		GT Combustion Filter Assy & Installation	3 days													
51		Electrical Installation	10 days													
52		Mechanical Installation	10 days													
53		Erect GTG 200	20 days													
54		Equipment Erection	10 days													
55		Generator	1 day													
56		Gas Turbine	1 day													
57		Air Inlet & Filter	3 days													
58		GT Roof Panel Assy & Installation	3 days													
59		GT Combustion Filter Assy & Installation	3 days													
60		Electrical Installation	10 days													
61		Mechanical Installation	10 days													
62		HV Installation	12 days													
63		Erect GSU's	12 days													
64		Install BOP Mechanical Eq.	33 days													
65		Install Oily Water Separator	5 days													
66		Install Instrument Air Compressor	2 days													
67		Install Fuel Gas Filter Skids	5 days													
68		Install U/G Piping Header System	20 days													
69		Install A/G Piping Header System	20 days													

Project: EDC LM6000 Project Executiv

Date: Thu 1/29/09

Task

Split

Progress

Milestone

Summary

Project Summary








External Tasks

External Milestone

Deadline

Page 3

EDC Project
LM6000 Simple Cycle Project
Project Executive Schedule

ID	Task Name	Duration														
			Month 1				Month 2				Month 3					
			Week 1	Week 2	Week 3	Week 4	Week 5	Week 6	Week 7	Week 8	Week 9	Week 10	Week 11	Week 12	Week 13	Week 14
70	 Install BOP Electrical Eq.	30 days														
71	 Install U/G Duct Banks	15 days														
72	 Install Elect Bldg Equipment & Aux Xfmrs	15 days														
73	Install Utility Bldg Equipment & Aux Xfmrs	15 days														
74	Install Ground Grid	15 days														
75	Install Cathodic Protection	15 days														
76	Install Area Lighting	15 days														
77	Commissioning and Startup	25 days														
78	BOP Commissioning	10 days														
79	GTG 100 Pre-Commissioning	10 days														
80	 Mechanical	10 days														
81	 Electrical	10 days														
82	GTG 200 Precommissioning	10 days														
83	 Mechanical	10 days														
84	 Electrical	10 days														
85	GTG 100 Commissioning	15 days														
86	GTG 200 Commissioning	15 days														
87	Sync to Grid	2 days														
88	GTG 100 Available	2 days														
89	GTG 200 Available	2 days														
90	Performance Testing	1 day														
91	GTG 100	1 day														
92	GTG 200	1 day														

Project: EDC LM6000 Project Executiv
Date: Thu 1/29/09

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress



Project Summary



Deadline

