

A B C D E F

1

2

3

4

5

SITE SAFETY LOGISTIC PLAN


FOR

53W53

53 WEST53 STREET, NEW YORK, NY 10019
BLOCK 1269, LOT 6, ZONING MAP XX
COMMUNITY BOARD: 105
BIN# 1813446

HEIGHT: 1114' TALL (77 STORY) CONCRETE STRUCTURE
MIXED USE BUILDING

D.O.B. #121-327-224 NB

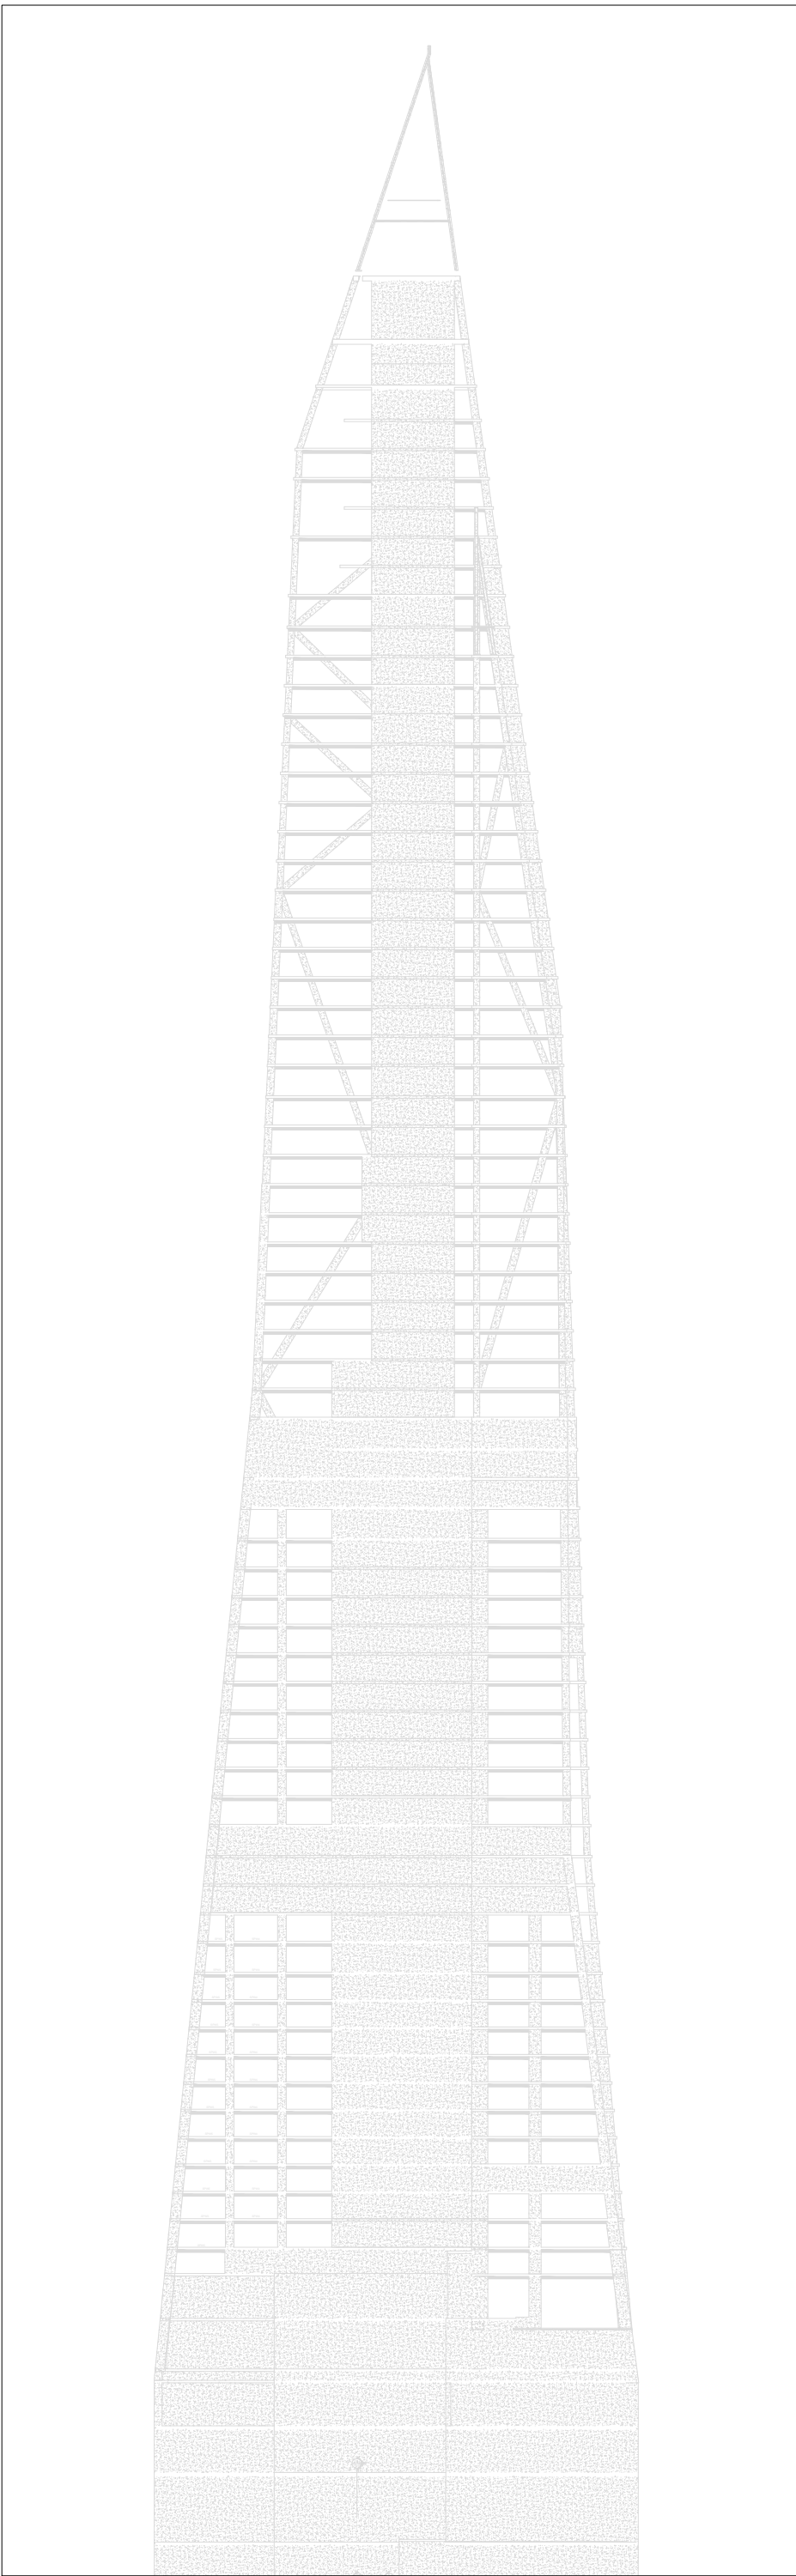

PREPARED BY:

LEND LEASE (US) CONSTRUCTION LMB, INC.
TECHNICAL SERVICES
LOGISTICS DEPARTMENT
TEL: 212-592-6973
E-MAIL: CALVIN.TORRES@LENDLEASE.COM

Lend Lease
200 PARK AVENUE
NEW YORK, NY 10166

32	08/20/18	TOH Phasing Revision
31	05/02/18	
30	04/23/18	
29	02/21/18	
28	01/25/18	
27	01/16/18	
26	10/18/17	
25	09/18/17	
24	07/31/17	
23	06/13/17	
22	05/17/17	
NO.	DATE	REVISION


PROJECT

53W53

A NEW BUILDING AT
53 West 53rd Street
New York, NY 10019

Title Cover

SEAL & SIGNATURE	DATE:	8/20/18
	PROJECT No.:	
	DRAWING BY:	CT
	CHECKED BY:	
	DWG No:	SSP-001.12
SCALE:	CADD FILE No:	PAGE No.:

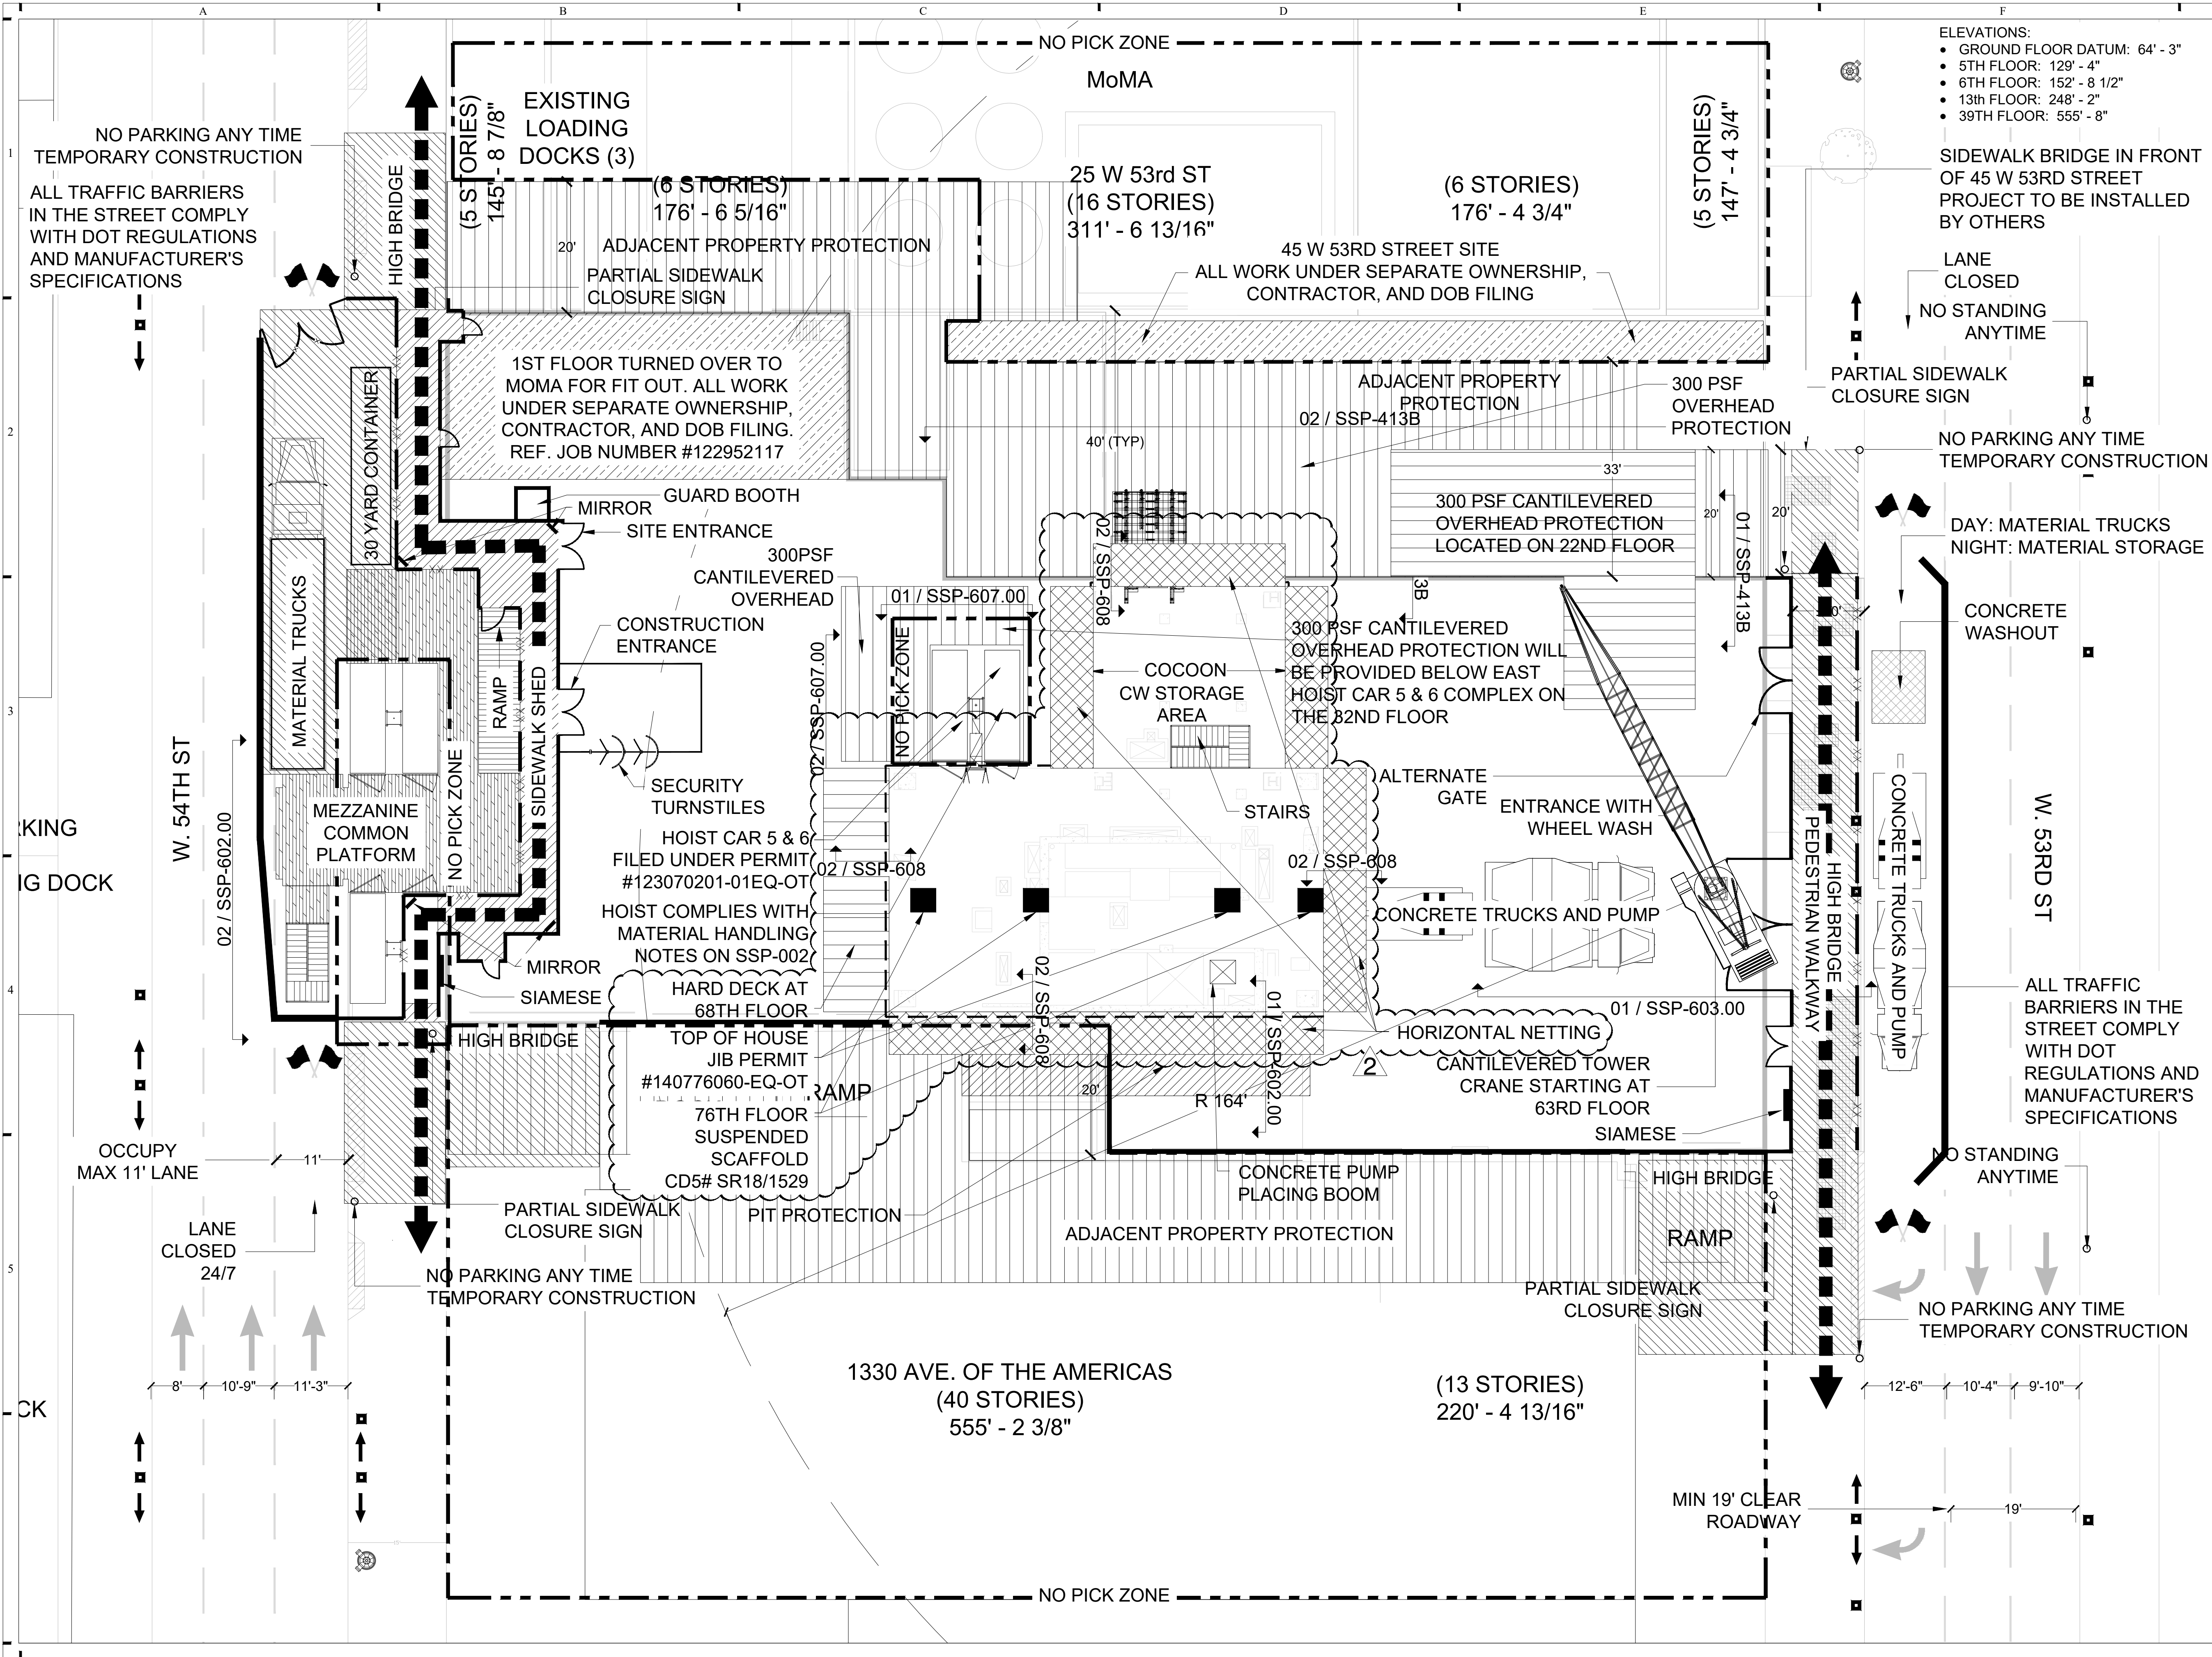

- ELEVATIONS:
- GROUND FLOOR DATUM: 64' - 3"
 - 5TH FLOOR: 129' - 4"
 - 6TH FLOOR: 152' - 8 1/2"
 - 13th FLOOR: 248' - 2"
 - 39TH FLOOR: 555' - 8"

SIDEWALK BRIDGE IN FRONT OF 45 W 53RD STREET PROJECT TO BE INSTALLED BY OTHERS

LANE CLOSED
NO STANDING ANYTIME

NO PARKING ANY TIME TEMPORARY CONSTRUCTION

DAY: MATERIAL TRUCKS
NIGHT: MATERIAL STORAGE

CONCRETE WASHOUT

W. 53RD ST

ALL TRAFFIC BARRIERS IN THE STREET COMPLY WITH DOT REGULATIONS AND MANUFACTURER'S SPECIFICATIONS

NO STANDING ANYTIME

NO PARKING ANY TIME TEMPORARY CONSTRUCTION

Lend Lease
200 PARK AVENUE
NEW YORK, NY 10166

- NOTES:
1. REFER TO DRAWING SSP-002 FOR LEGEND.
 2. REFER TO DRAWING SSP-002 FOR GENERAL NOTES.
 3. FOR TYPICAL DETAILS, PLEASE REFER TO SHEET SSP-710, SSP-720, SSP-730 & SSP-740.
 4. VERTICAL ENCLOSURE SYSTEM (COCOON) TO BE USED. DETAILS TO BE FILED SEPARATELY.
 5. SIDEWALK SHED TO BE INSTALLED WHEN THE BUILDING REACHES THE 2ND FLOOR.
 6. TEMPORARY STANDPIPE SHALL BE INSTALLED AND OPERATIONAL WHEN THE BUILDING HEIGHT REACHES 75'-0".
 7. TEMPORARY STAIR TOWERS MAY BE RELOCATED TO SUIT THE CONSTRUCTION MANAGER'S LOGISTICS REQUIREMENTS. TWO MEANS OF EGRESS WILL BE MAINTAINED AT ALL TIMES.
 8. SIGNAL MEN TO STOP PEDESTRIAN TRAFFIC IN WALKWAY DURING PICKING AND SWINGING LOADS (TYP).
 9. OVERHEAD PROTECTION AND ADJACENT PROPERTY PROTECTION WILL BE INSTALLED PRIOR TO BUILDING REACHING THE HEIGHT OF ADJACENT BUILDING.
 10. THE EAST SHEAR WALL FORMWORK, AT THE 45 W 53RD STREET PROPERTY LINE SHALL BE JUMPED WHEN NO CONSTRUCTION ACTIVITIES ARE ONGOING AT THE ADJACENT PROPERTY.
 11. CONCRETE WASHOUT BOX LOCATIONS TO CHANGE AT CONSTRUCTION MANAGER'S DISCRETION PENDING SITE LOGISTICS.
 12. EAST HOIST COMPLEX CARS 5 & 6 WILL BE INSTALLED OFF A CANTILEVERED PLATFORM ON THE 32ND OR 33RD FLOOR WITH THE HOIST STARTING TO SERVICE FLOORS ON THE 34TH FLOOR. TIMING OF INSTALLATION OF HOIST SHALL BE DETERMINED BY PROJECT LOGISTICS REQUIREMENTS.
 13. 300 PSF UDL CANTILEVERED PROTECTION SHALL BE PROVIDED BELOW HOIST 5 & 6 PLATFORMS IN AREAS WHERE THE BUILDING IS NOT ENCLOSED.
 14. PERI LOADING PLATFORMS SHOWN FOR DIAGRAM PURPOSES ONLY. ACTUAL LOCATION OF THE LIFTING PLATFORM SUBJECT TO CHANGE PER THE ENGINEERED PERI COCOON DRAWINGS.


- LIST OF EQUIPMENT:
- TOWER CRANE
 - [3] DUAL HOISTS
 - CONCRETE TRUCKS
 - WELDING MACHINES
 - MAN LIFTS
 - SCISSOR LIFTS
 - ZOOM BOOMS
 - CONCRETE PUMP
 - CONCRETE PLACING BOOM
 - T BOOMS
 - MONORAILS
 - CURTAIN WALL CRABS

NO.	DATE	REVISION
2	08/20/18	TOH Phasing Revision
1	01/25/18	TOH Phasing Revision
0	01/16/18	TOH Phasing

53W53

A NEW BUILDING AT
53 West 53rd Street
New York, NY 10019

Superstructure - Phase 5B
Floors 73-76

SEAL & SIGNATURE: 
DATE: 8/20/18
PROJECT No.:
DRAWING BY: CT
CHECKED BY:
DWG No: **SSP-451.00**
CADO FILE No: PAGE No:
