EDC LaRosa Addition Project
LM6000 Simple Cycle Project
Project Executive Schedule

ID	Task Name	Duration	Start	Finish
1	**EDC - LaRosa Phase II Project - 2 Unit LM6000 SPR**	**xxx days**	**Thu 6/10/10**	**Fri 2/18/11**
2	**Initial Date**	**1 day**	Thu 6/10/10	Thu 6/10/10
3	**Milestone Dates (Key Dates)**	**22 days**	**Thu 6/10/10**	Fri 7/9/10
4	Initial Date	1 day	Thu 6/10/10	Thu 6/10/10
5	Backfeed Power Available	1 day	Wed 6/30/10	Wed 6/30/10
6	Natural Gas Available	1 day	Thu 7/1/10	Thu 7/1/10
7	Raw Water Available	1 day	Fri 7/2/10	Fri 7/2/10
8	Telephone & Internet Service Available	1 day	Thu 6/10/10	Thu 6/10/10
9	Construction Power Connection Available	1 day	Thu 6/10/10	Thu 6/10/10
10	Construction Permit	1 day	Thu 6/10/10	Thu 6/10/10
11	**Engineering**	**55 days**	**Fri 6/11/10**	**Wed 8/4/10**
12	Conceptual & Major Equipment Specs	10 days	Fri 6/11/10	Sun 6/20/10
13	Site survey	4 days	Mon 6/21/10	Thu 6/24/10
14	Issue Foundation for Construction Drawings	10 days	Fri 6/25/10	Fri 7/9/10
15	Detailed Engineering	60 days	Mon 6/21/10	Fri 7/30/10
16	Bulk Material Specs and PO's	30 days	Mon 6/21/10	Tue 7/20/10
17	Issue for Construction Drawings	5 days	Sat 7/31/10	Wed 8/4/10
18	**Procurement**	**90 days**	**Mon 6/21/10**	**Sat 9/18/10**
19	Buildings	12 wks	Mon 6/21/10	Thu 8/19/10
20	BOP Mechanical	12 wks	Wed 7/21/10	Sat 9/18/10
21	BOP Electrical	12 wks	Wed 7/21/10	Sat 9/18/10
22	**Transportation**	**90 days**	**Thu 6/10/10**	**Tue 9/7/10**
23	GTG Package 100	30 days	Thu 6/10/10	Fri 7/9/10
24	GTG Package 200	30 days	Thu 6/10/10	Fri 7/9/10
25	GSU's	90 days	Thu 6/10/10	Tue 9/7/10
26	**Construction**	**129 days**	**Wed 6/30/10**	**Fri 11/5/10**
27	**Mobilize to Site**	**14 days**	Wed 6/30/10	Tue 7/13/10
28	**Civil Work**	**20 days**	**Wed 7/14/10**	**Mon 8/2/10**
29	Site Preparation	10 days	Wed 7/14/10	Fri 7/23/10
30	Excavation & Undging	10 days	Sat 7/24/10	Mon 8/2/10
31	**Power Island Foundations**	**25 days**	**Tue 8/3/10**	**Fri 8/27/10**
32	GTG 100	15 days	Tue 8/3/10	Tue 8/17/10
33	GTG 200	15 days	Tue 8/3/10	Tue 8/17/10
34	GSU 100	10 days	Wed 8/18/10	Fri 8/27/10
35	GSU 200	10 days	Wed 8/18/10	Fri 8/27/10
36	**BOP Foundations**	**25 days**	**Tue 8/3/10**	**Fri 8/27/10**
37	Unit building	10 days	Tue 8/3/10	Thu 8/12/10
38	Substation	10 days	Tue 8/3/10	Thu 8/12/10
39	Substation Bldg	10 days	Fri 8/13/10	Sun 8/22/10
40	Pipe Racks	10 days	Wed 8/18/10	Fri 8/27/10
41	**Building Erection & Fit-out**	**15 days**	**Fri 8/13/10**	**Fri 9/27/10**
42	Unit Building	10 days	Fri 8/13/10	Sun 8/22/10
43	Erect Substation Bldg	5 days	Mon 8/23/10	Fri 8/27/10
44	**Erect GTG 100**	**90 days**	**Wed 8/18/10**	**Fri 11/5/10**
45	**Equipment Erection**	**20 days**	**Wed 8/18/10**	**Mon 9/6/10**
46	Generator	2 days	Wed 8/18/10	Thu 8/19/10
47	Gas Turbine	2 days	Fri 8/20/10	Sat 8/21/10
48	Air Inlet & Filter	6 days	Fri 8/20/10	Wed 8/25/10
49	GT Roof Panel Assy & Installation	6 days	Thu 8/26/10	Tue 8/31/10
50	GT Combustion Filter Assy & Installation	6 days	Wed 9/1/10	Mon 9/6/10
51	Electrical Installation	60 days	Tue 9/7/10	Fri 11/5/10
52	Mechnical Installation	60 days	Tue 9/7/10	Fri 11/5/10
53	**Erect GTG 200**	**90 days**	**Wed 8/18/10**	**Fri 11/5/10**
54	**Equipment Erection**	**20 days**	**Wed 8/18/10**	**Mon 9/6/10**
55	Generator	2 days	Wed 8/18/10	Thu 8/19/10
56	Gas Turbine	2 days	Fri 8/20/10	Sat 8/21/10
57	Air Inlet & Filter	6 days	Fri 8/20/10	Wed 8/25/10
58	GT Roof Panel Assy & Installation	6 days	Thu 8/26/10	Tue 8/31/10
59	GT Combustion Filter Assy & Installation	6 days	Wed 9/1/10	Mon 9/6/10
60	Electrical Installation	60 days	Tue 9/7/10	Fri 11/5/10
61	Mechnical Installation	60 days	Tue 9/7/10	Fri 11/5/10
62	BOP Installation	95 days	Tue 8/3/10	Fri 11/5/10
63	**Commissioning and Startup**	**40 days**	**Mon 11/8/10**	**Fri 12/31/10**
64	BOP Commissioning	20 days	Mon 11/8/10	Fri 12/3/10
65	**GTG 100 Pre-Commissioning**	**15 days**	**Mon 11/8/10**	**Fri 11/26/10**
66	Mechanical	15 days	Mon 11/8/10	Fri 11/26/10
67	Electrical	15 days	Mon 11/8/10	Fri 11/26/10
68	**GTG 200 Precommissioning**	**10 days**	**Mon 11/29/10**	**Fri 12/10/10**
69	Mechanical	10 days	Mon 11/29/10	Fri 12/10/10
70	Electrical	10 days	Mon 11/29/10	Fri 12/10/10
71	GTG 100 Commissioning	15 days	Mon 12/13/10	Fri 12/31/10
72	GTG 200 Commissioning	15 days	Mon 12/13/10	Fri 12/31/10
73	**Sync to Grid**	**2 days**	**Mon 1/3/11**	**Tue 1/4/11**
74	GTG 100 Available	2 days	Mon 1/3/11	Tue 1/4/11
75	GTG 200 Available	2 days	Mon 1/3/11	Tue 1/4/11
76	**Performance Testing**	**3 days**	**Wed 1/5/11**	**Fri 1/7/11**
77	GTG 100	3 days	Wed 1/5/11	Fri 1/7/11
78	GTG 200	3 days	Wed 1/5/11	Fri 1/7/11
79	Project Clean-up & demobilization	30 days	Mon 1/10/11	Fri 2/18/11

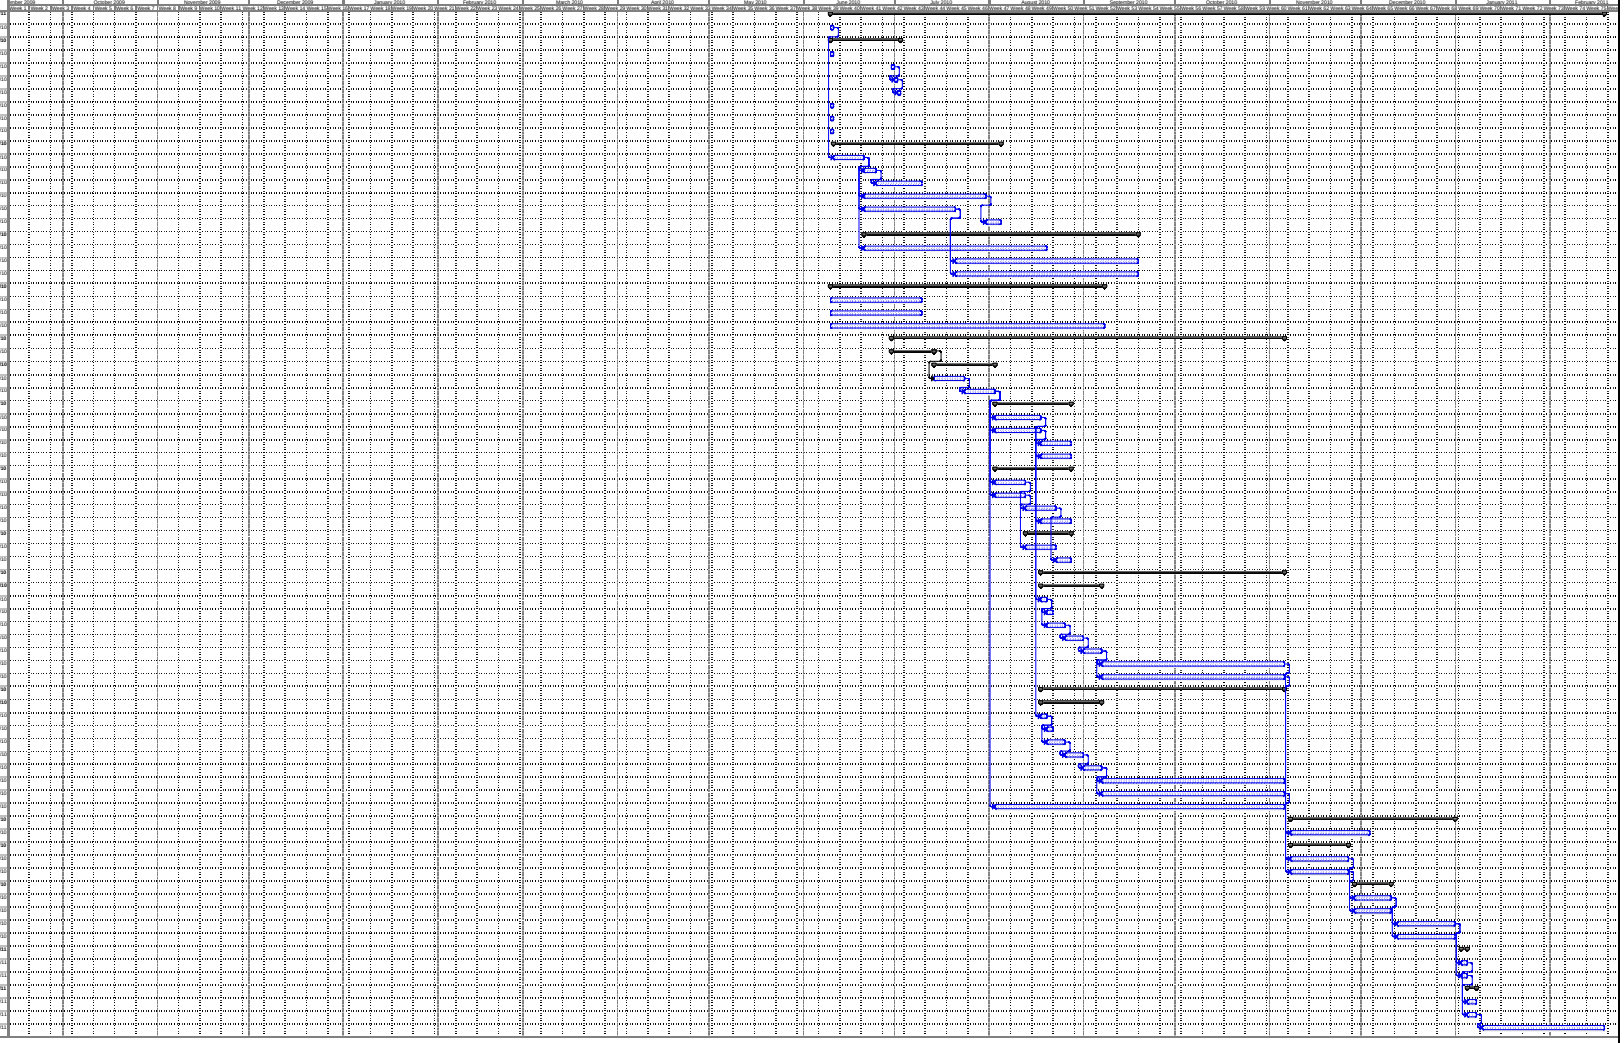

Project: EDC LaRosa Addition LM600 Date: Thu 6/10/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split
